


SHOTBLAST MACHINE NO. 1 DISMANTLING PLAN

Jhoremil Cabrillos CTU-MAIN BSME 4

MACHINE OVERVIEW

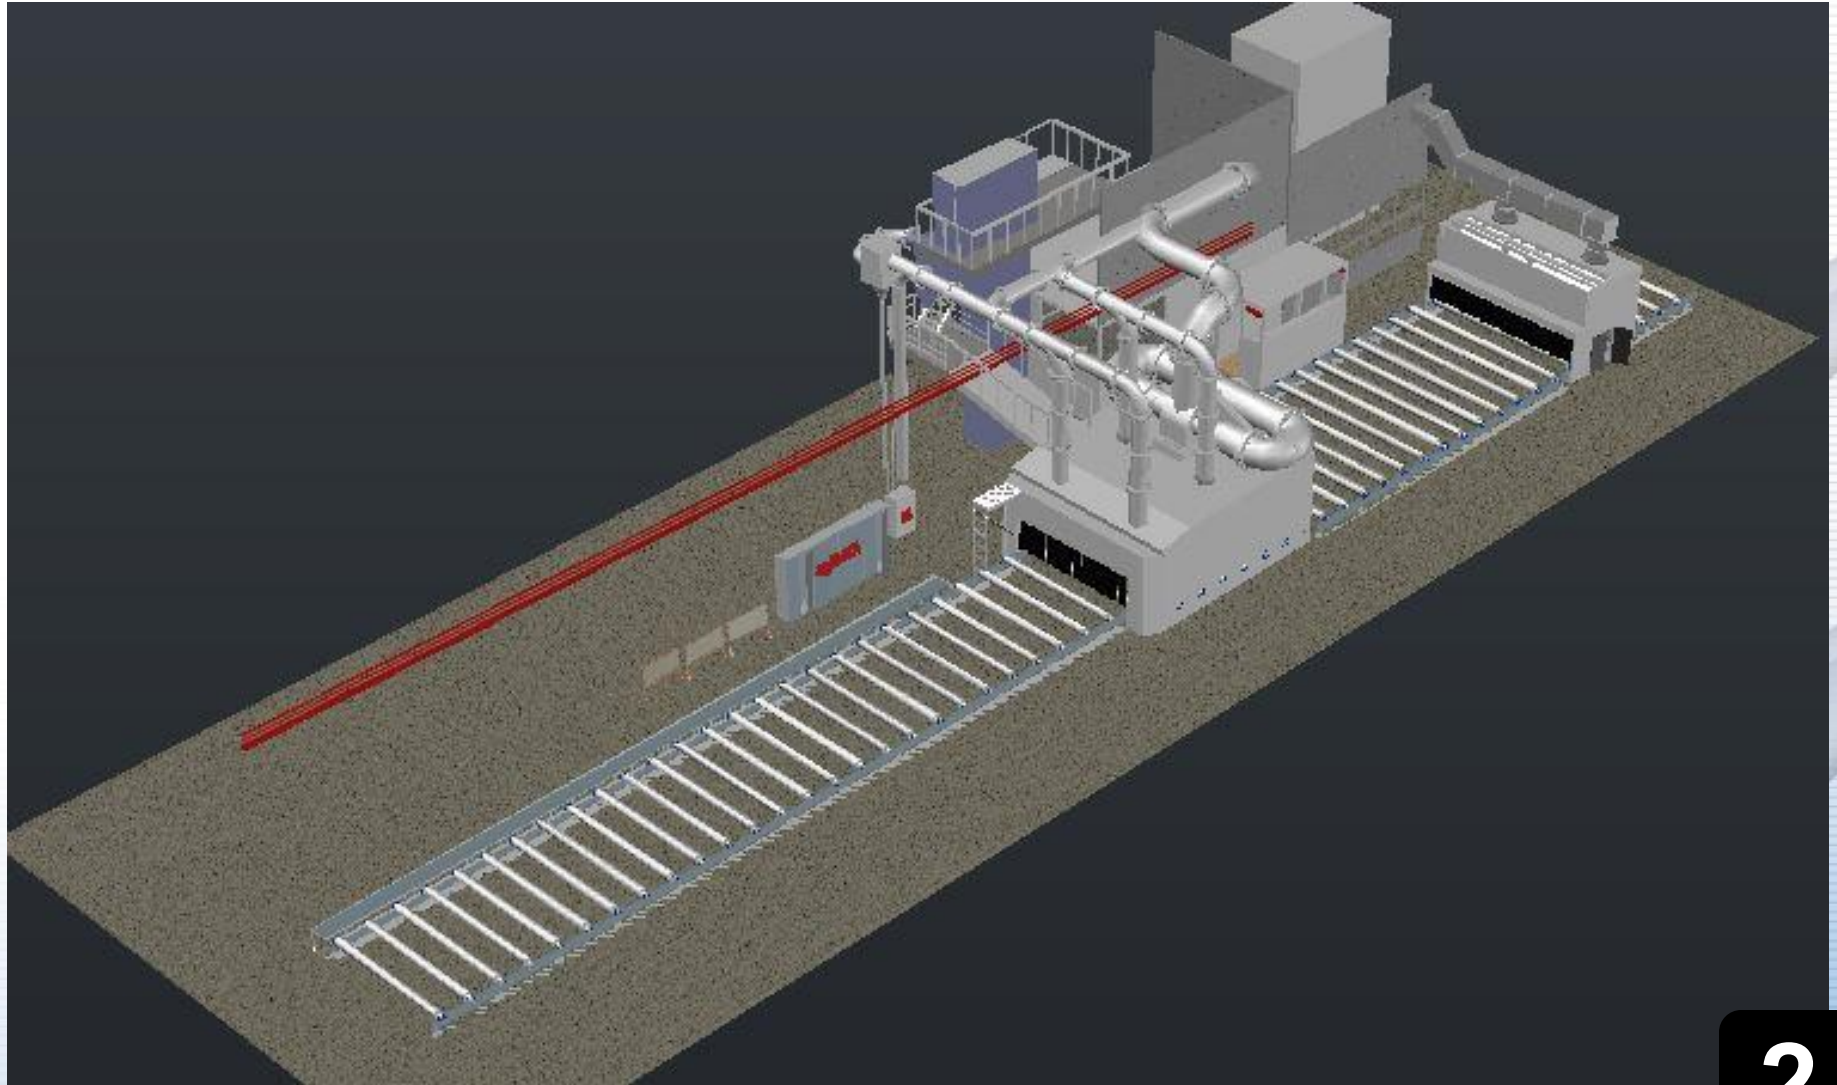

PHASE 1

- ☐ Disconnection and removal of supply and control panel
- ☐ Segregation and disposal of all wires
- ☐ Removal of motors and fans/blowers


NO. OF DAYS:

2 DAYS


NO. OF WORKERS:

4 ELECTRICAL | 2 MECHANICAL

MACHINE OVERVIEW

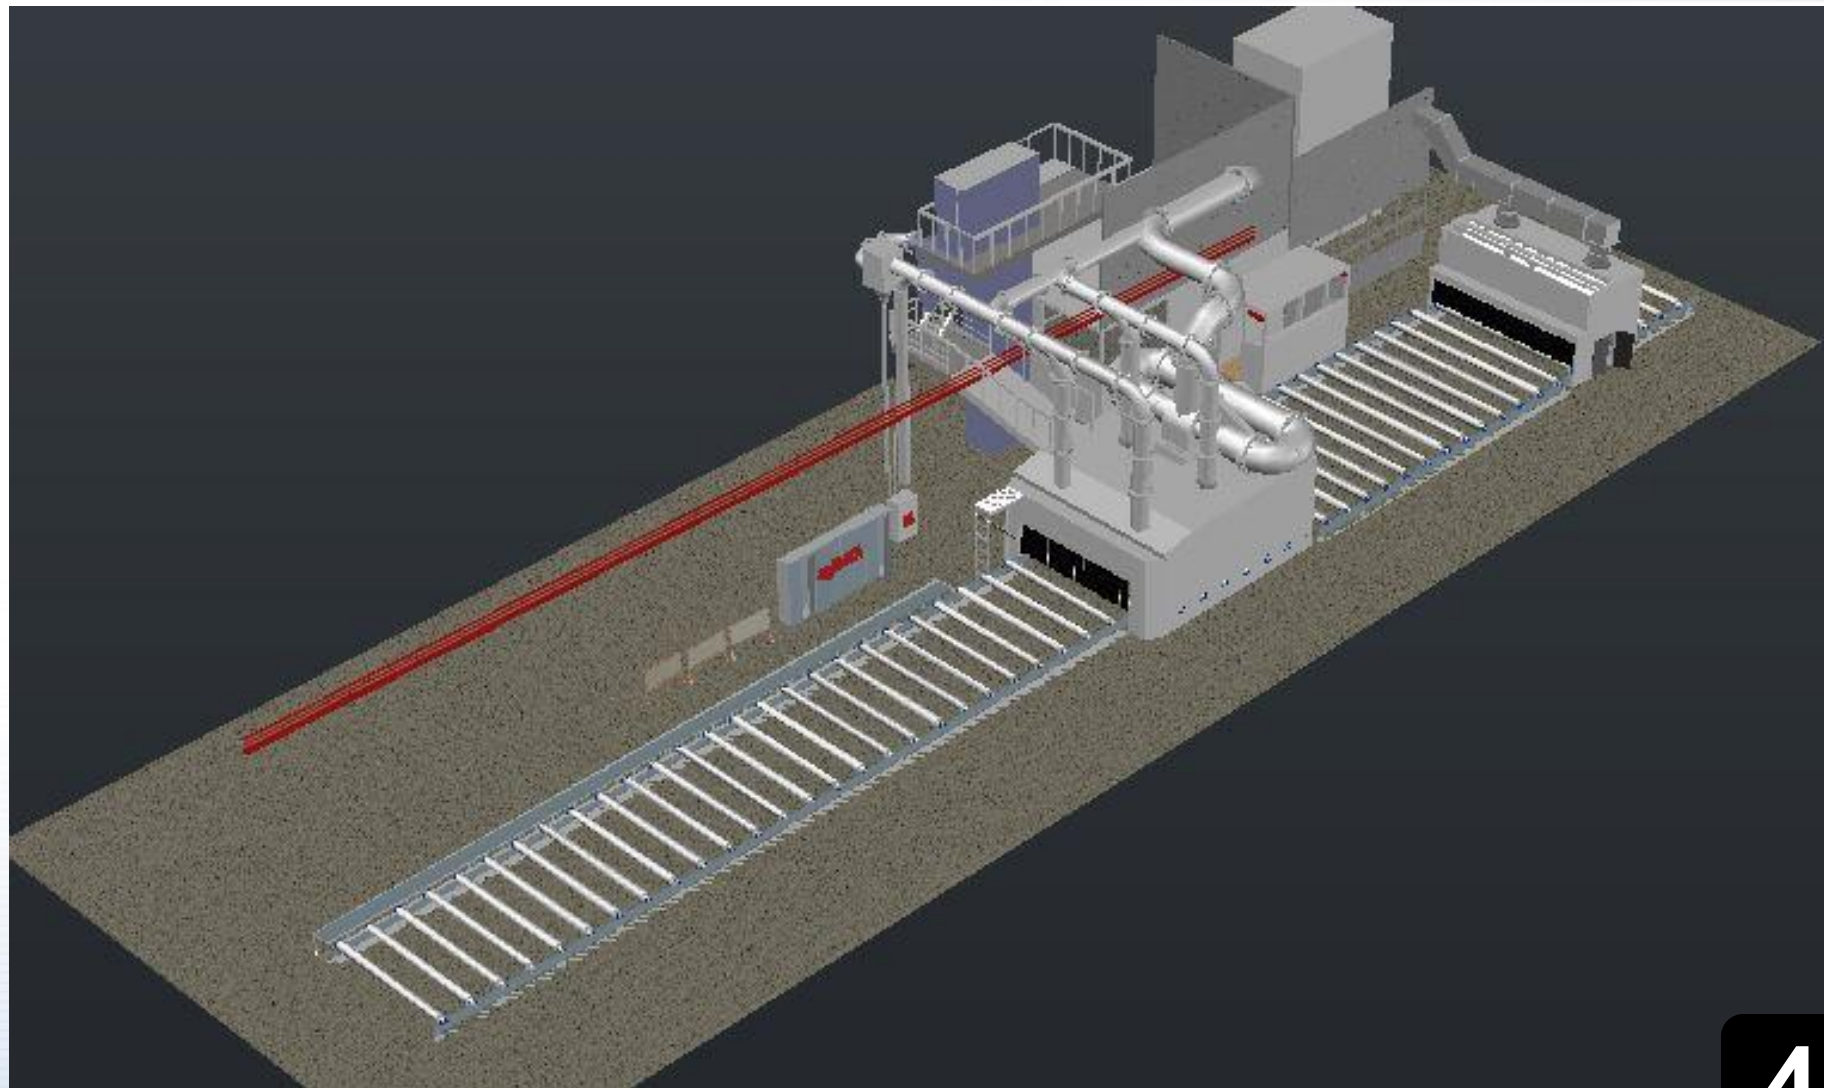

PHASE 1

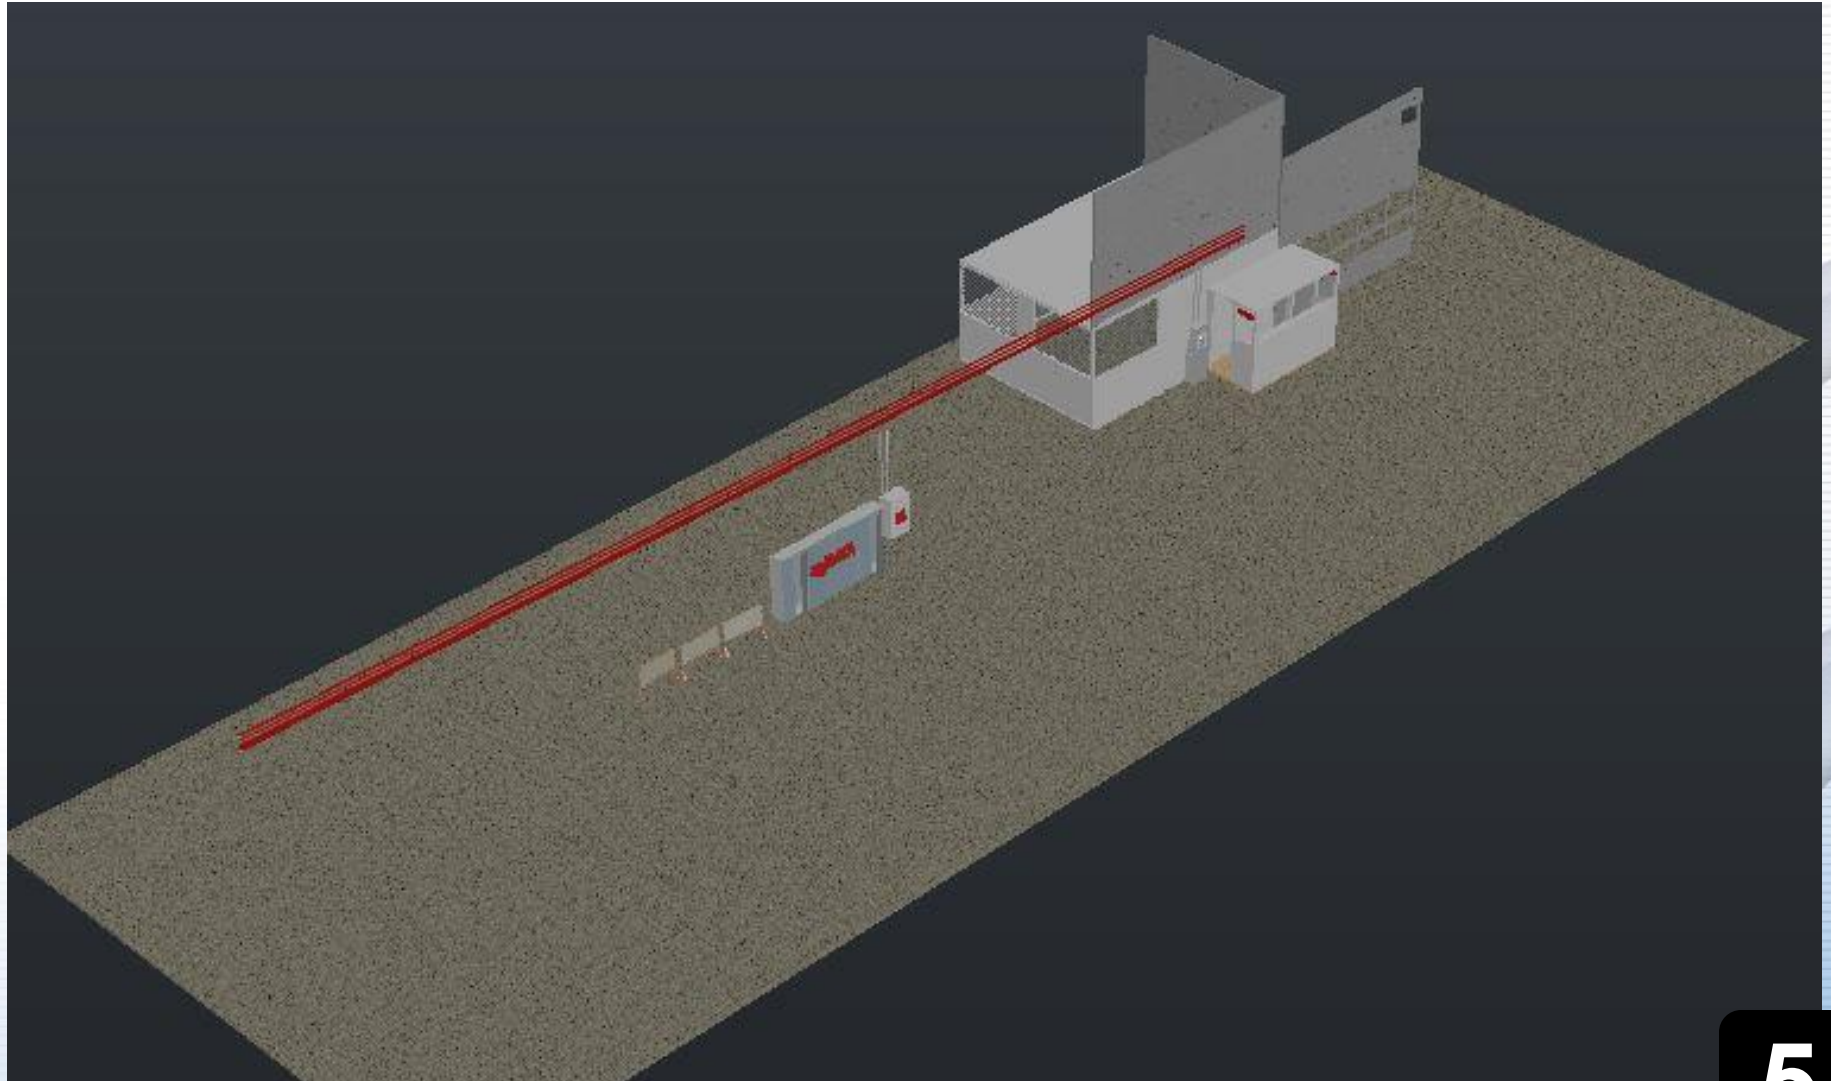

Supply Panel



Control Panel



Wires



Conveyor motor



Motor in dust collector



Fans above SB room



PHASE 2

- ❑ Removal of outside roller conveyor including chain guard and supports


NO. OF DAYS:

4 DAYS


NO. OF WORKERS:

5 MECHANICAL | 1 ELECTRICAL

MACHINE OVERVIEW

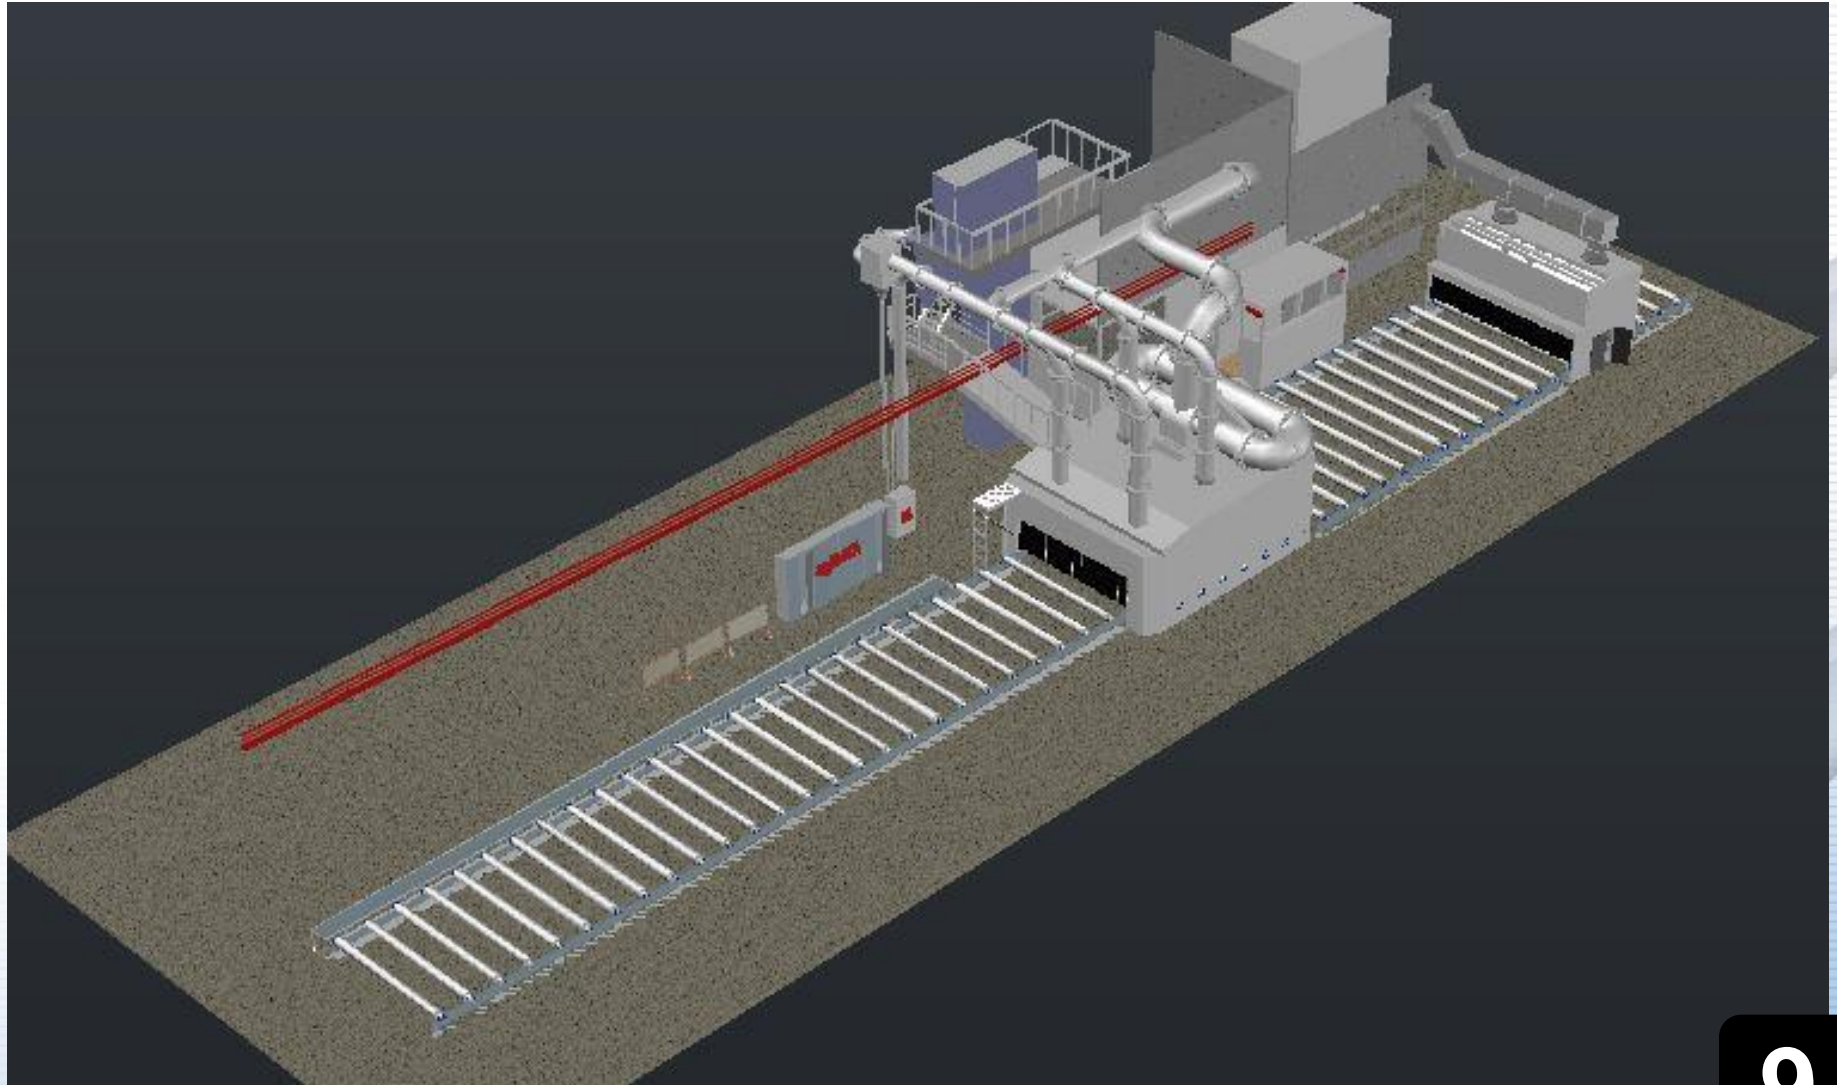

PHASE 2

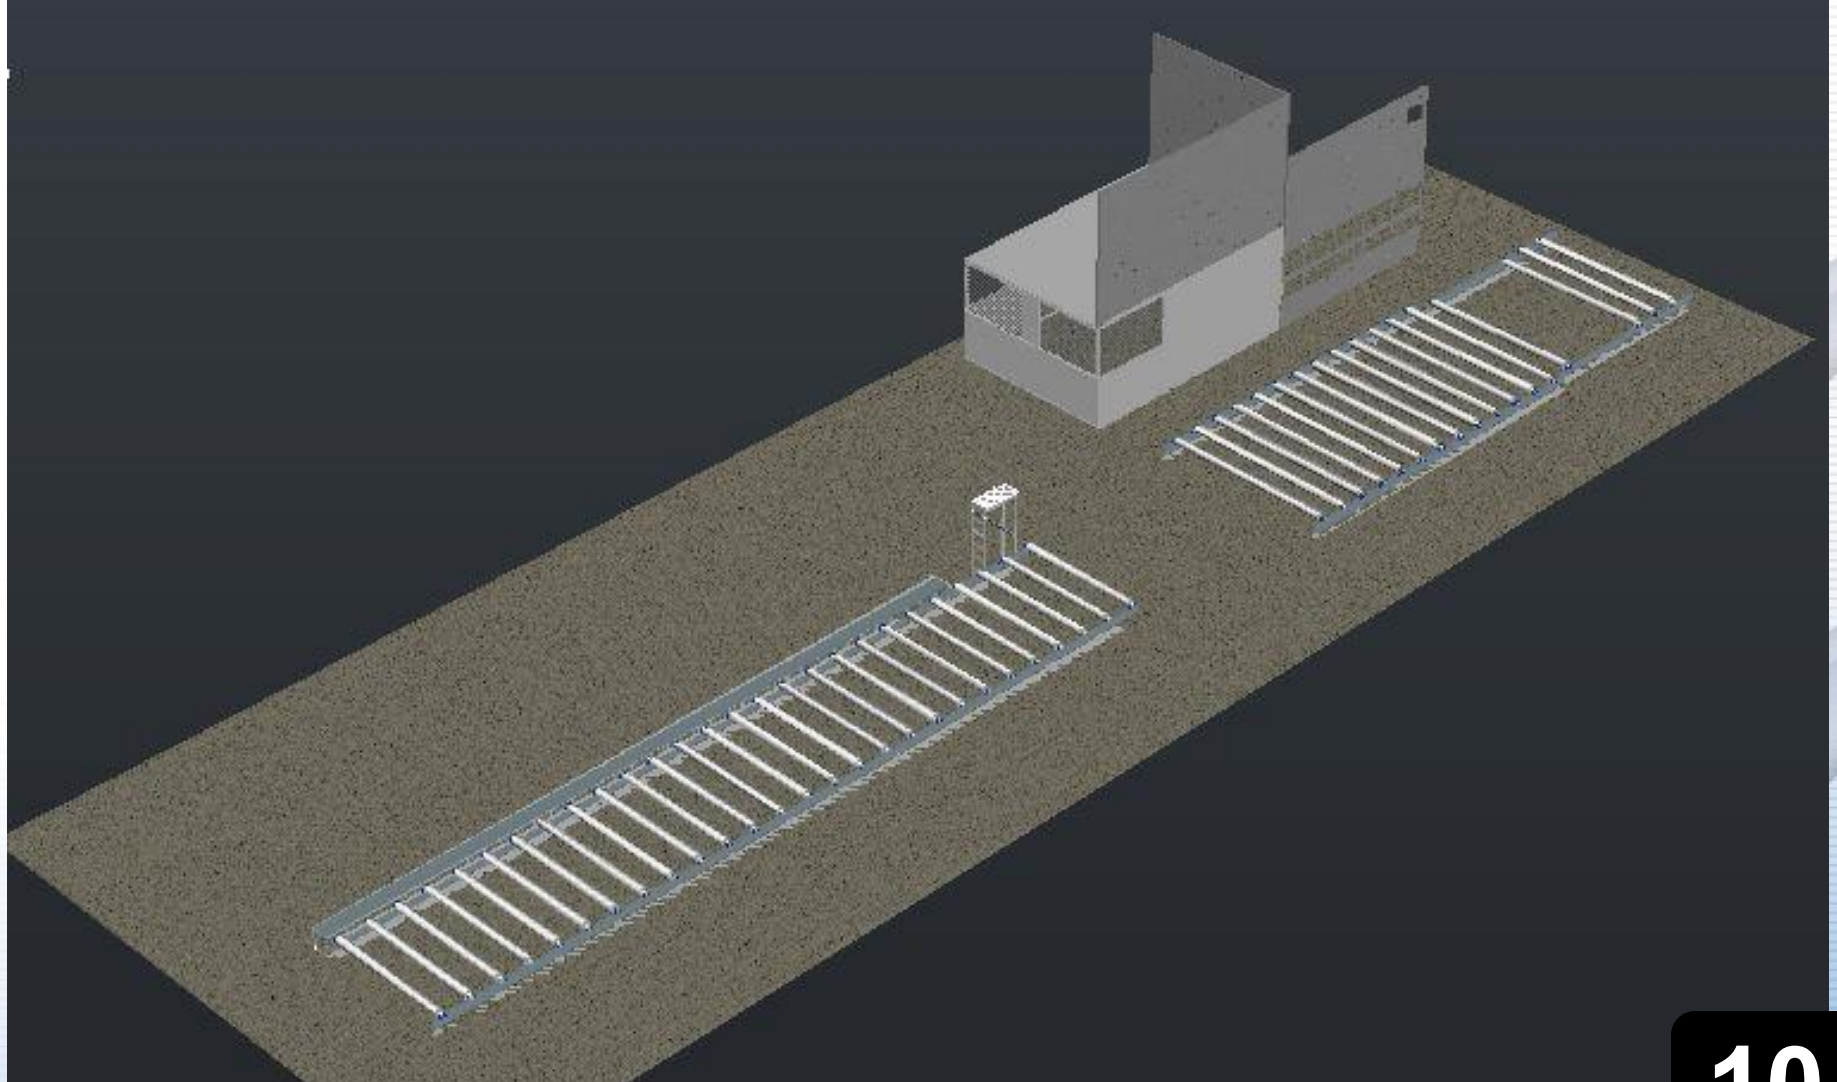



Pillow block



Stand connection



PHASE 3

- ❑ Removal of ducting in shotblast and paint machine
- ❑ Removal of bucket elevator from top to floor including screw conveyor


NO. OF DAYS:

6 DAYS


NO. OF WORKERS:

5 MECHANICAL | 1 ELECTRICAL


MACHINE OVERVIEW

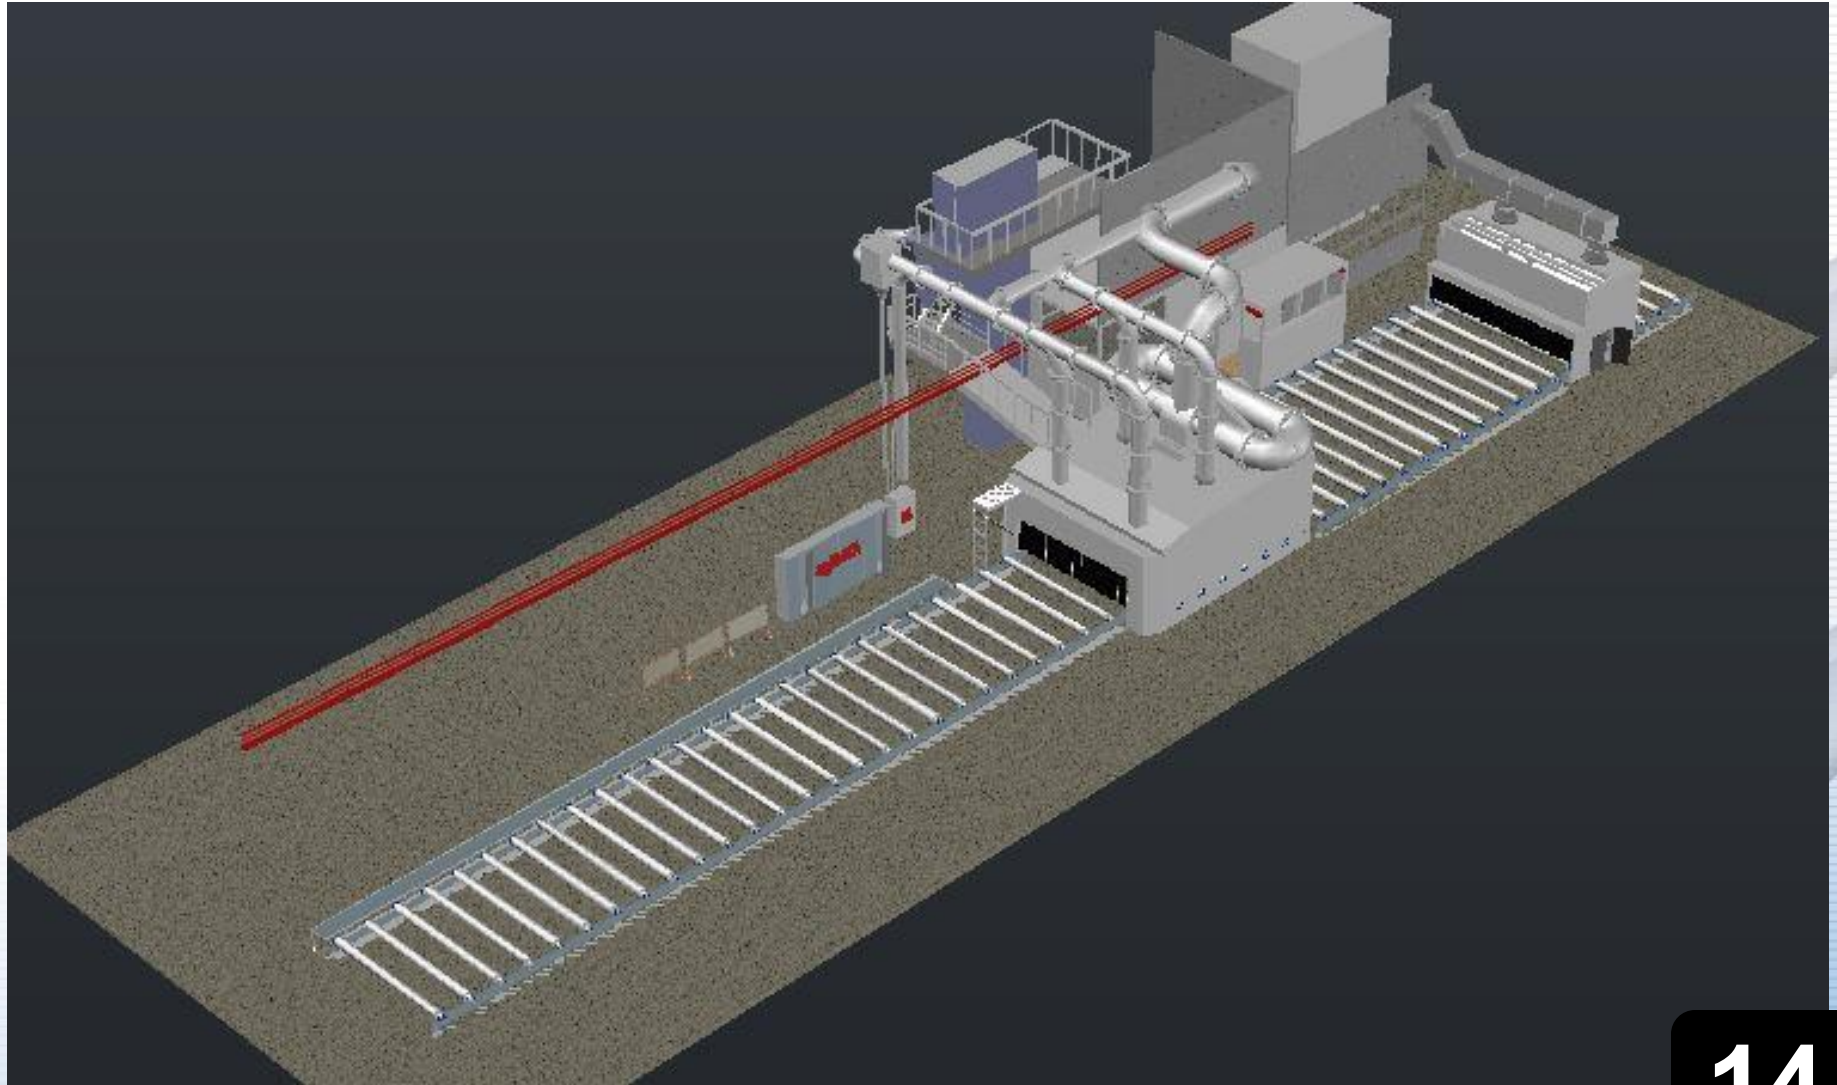


PHASE 3

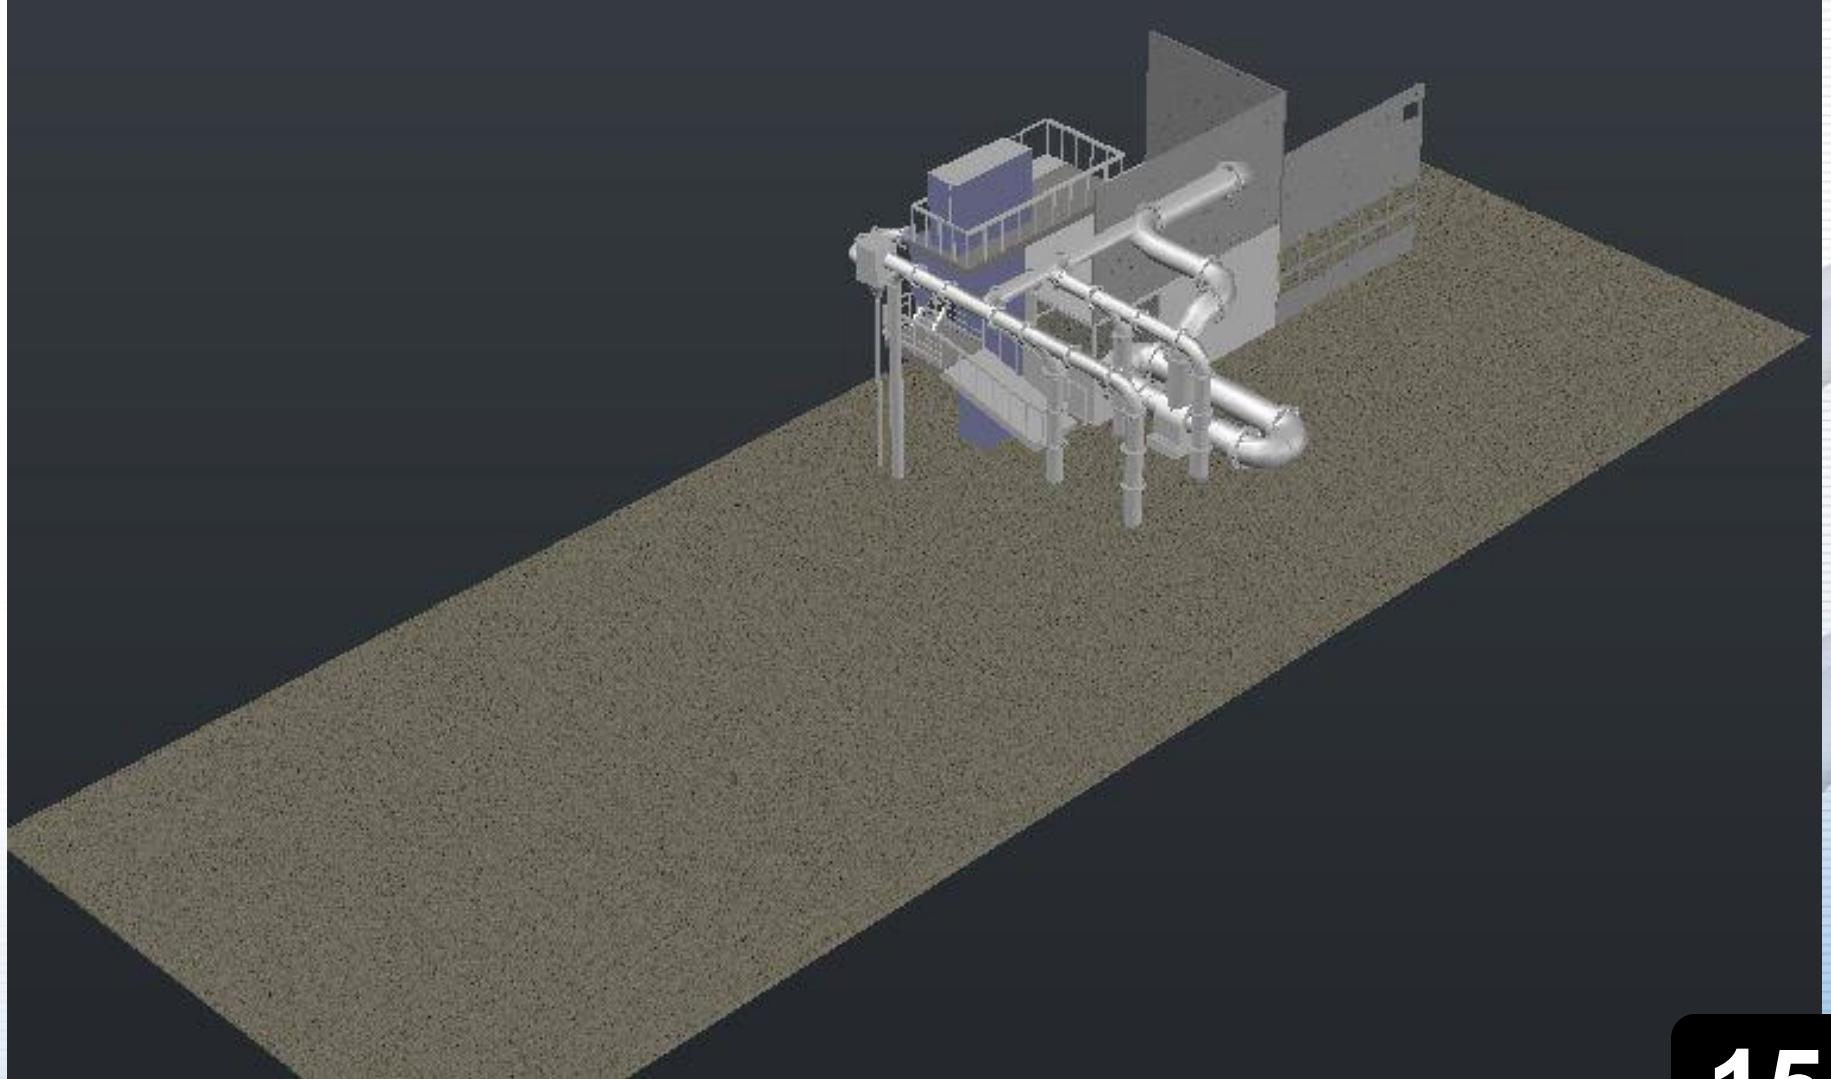

Ducting

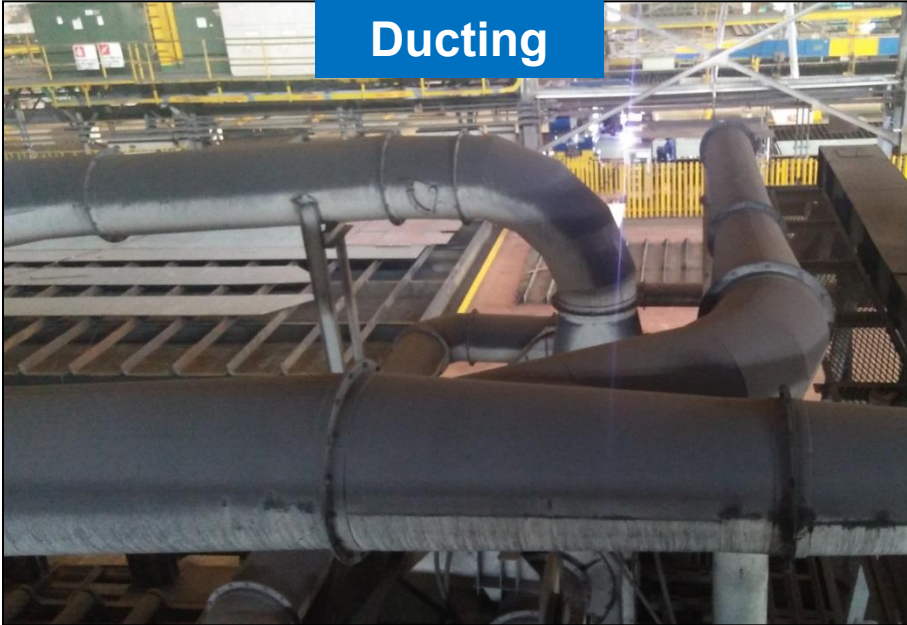

Bolt Coupling

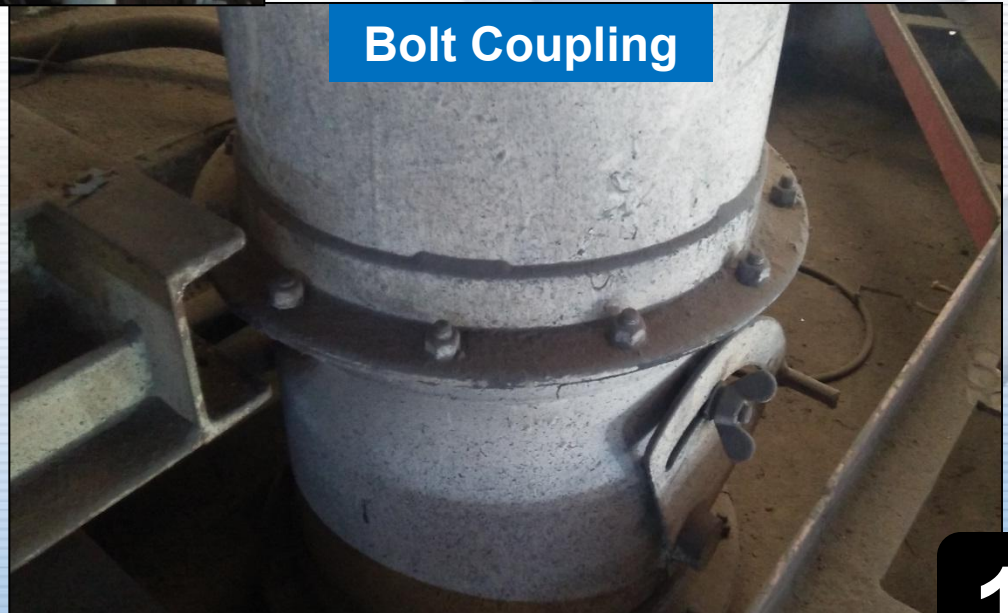


SB to dust collector



Paint machine to dust collector



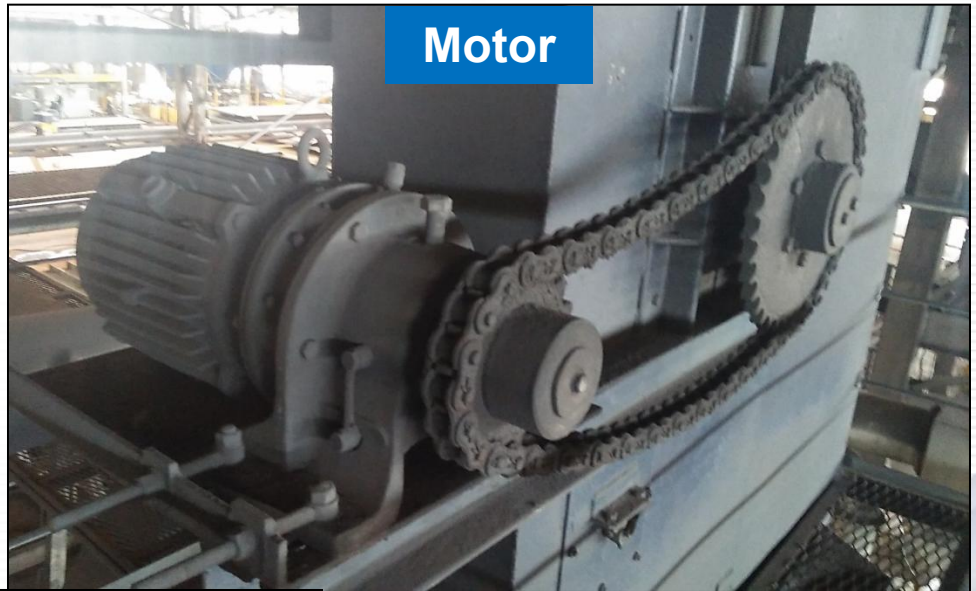

Motor



Screw conveyor



Bucket elevator



Floor level

PHASE 4

- ❑ Removal of shotblast machine from top to bottom including inside screw and roller conveyor
- ❑ Removal of remaining parts of bucket elevator and steel sheet flooring


NO. OF DAYS:

6 DAYS


NO. OF WORKERS:

5 MECHANICAL | 1 ELECTRICAL

MACHINE OVERVIEW

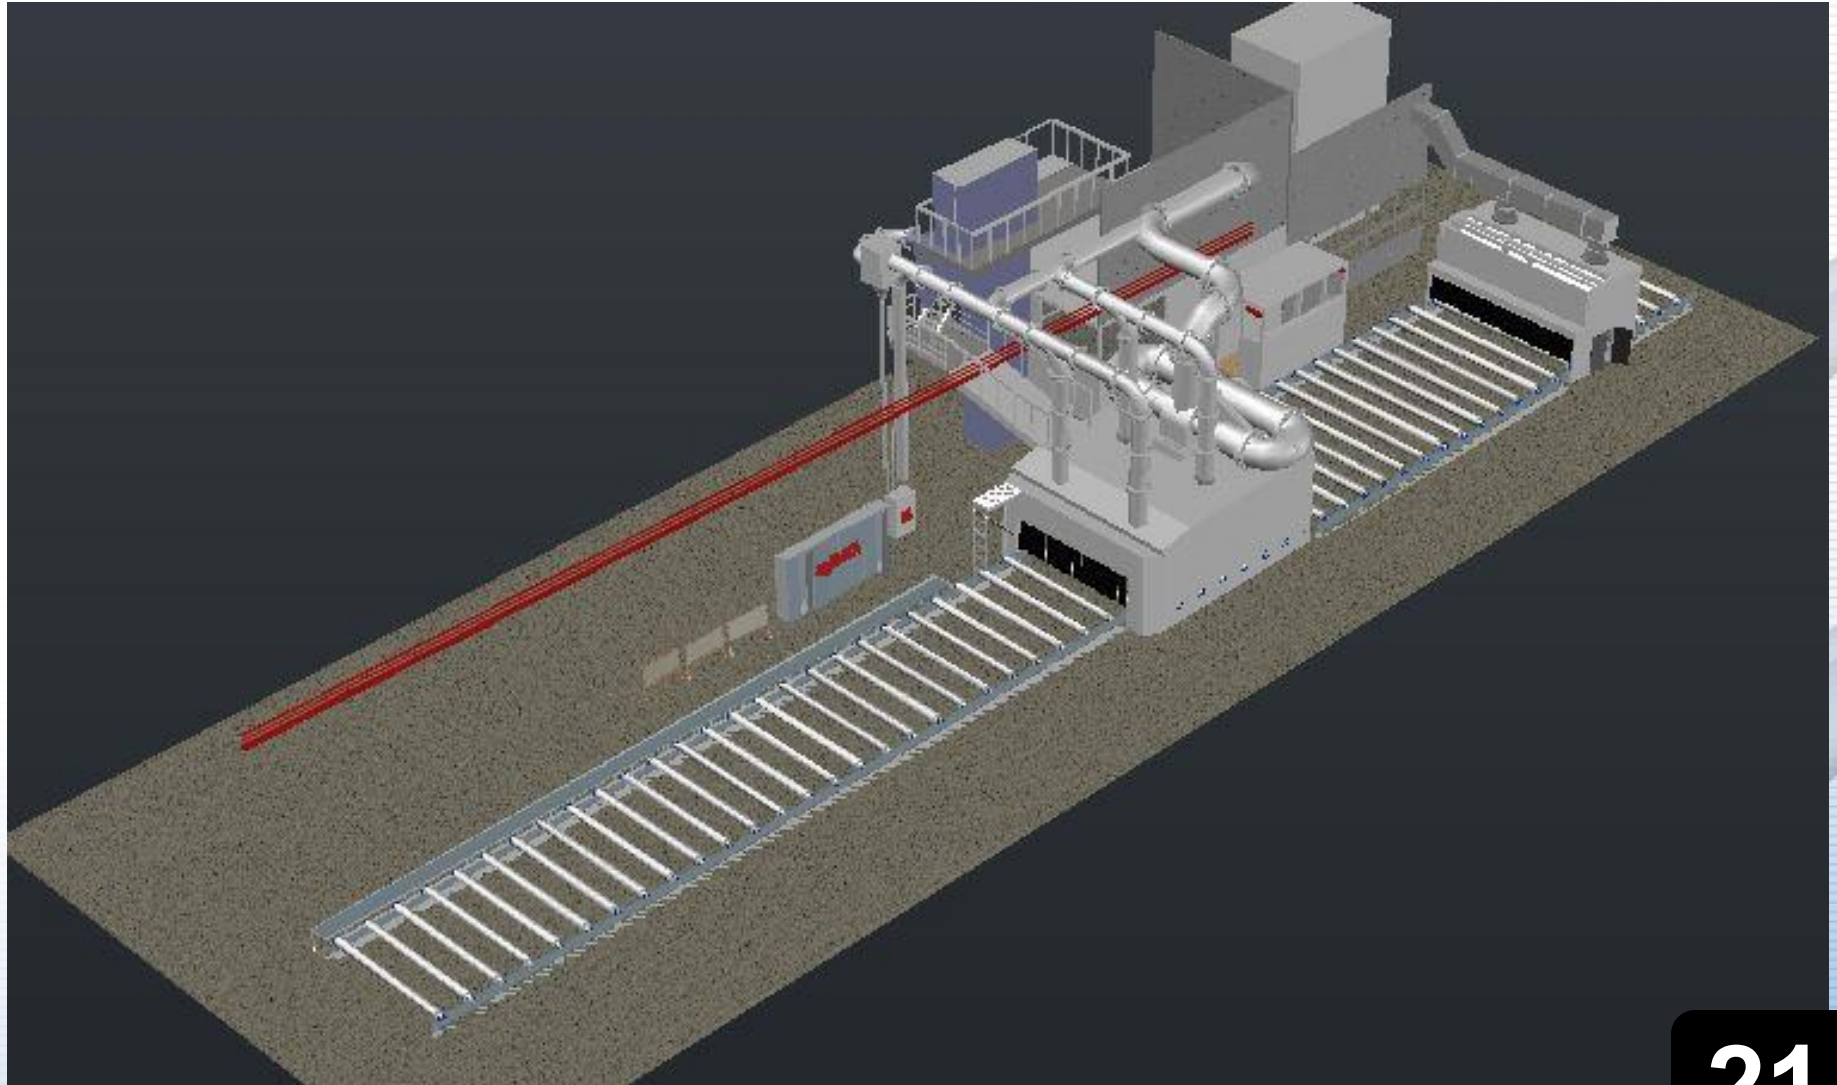

PHASE 4

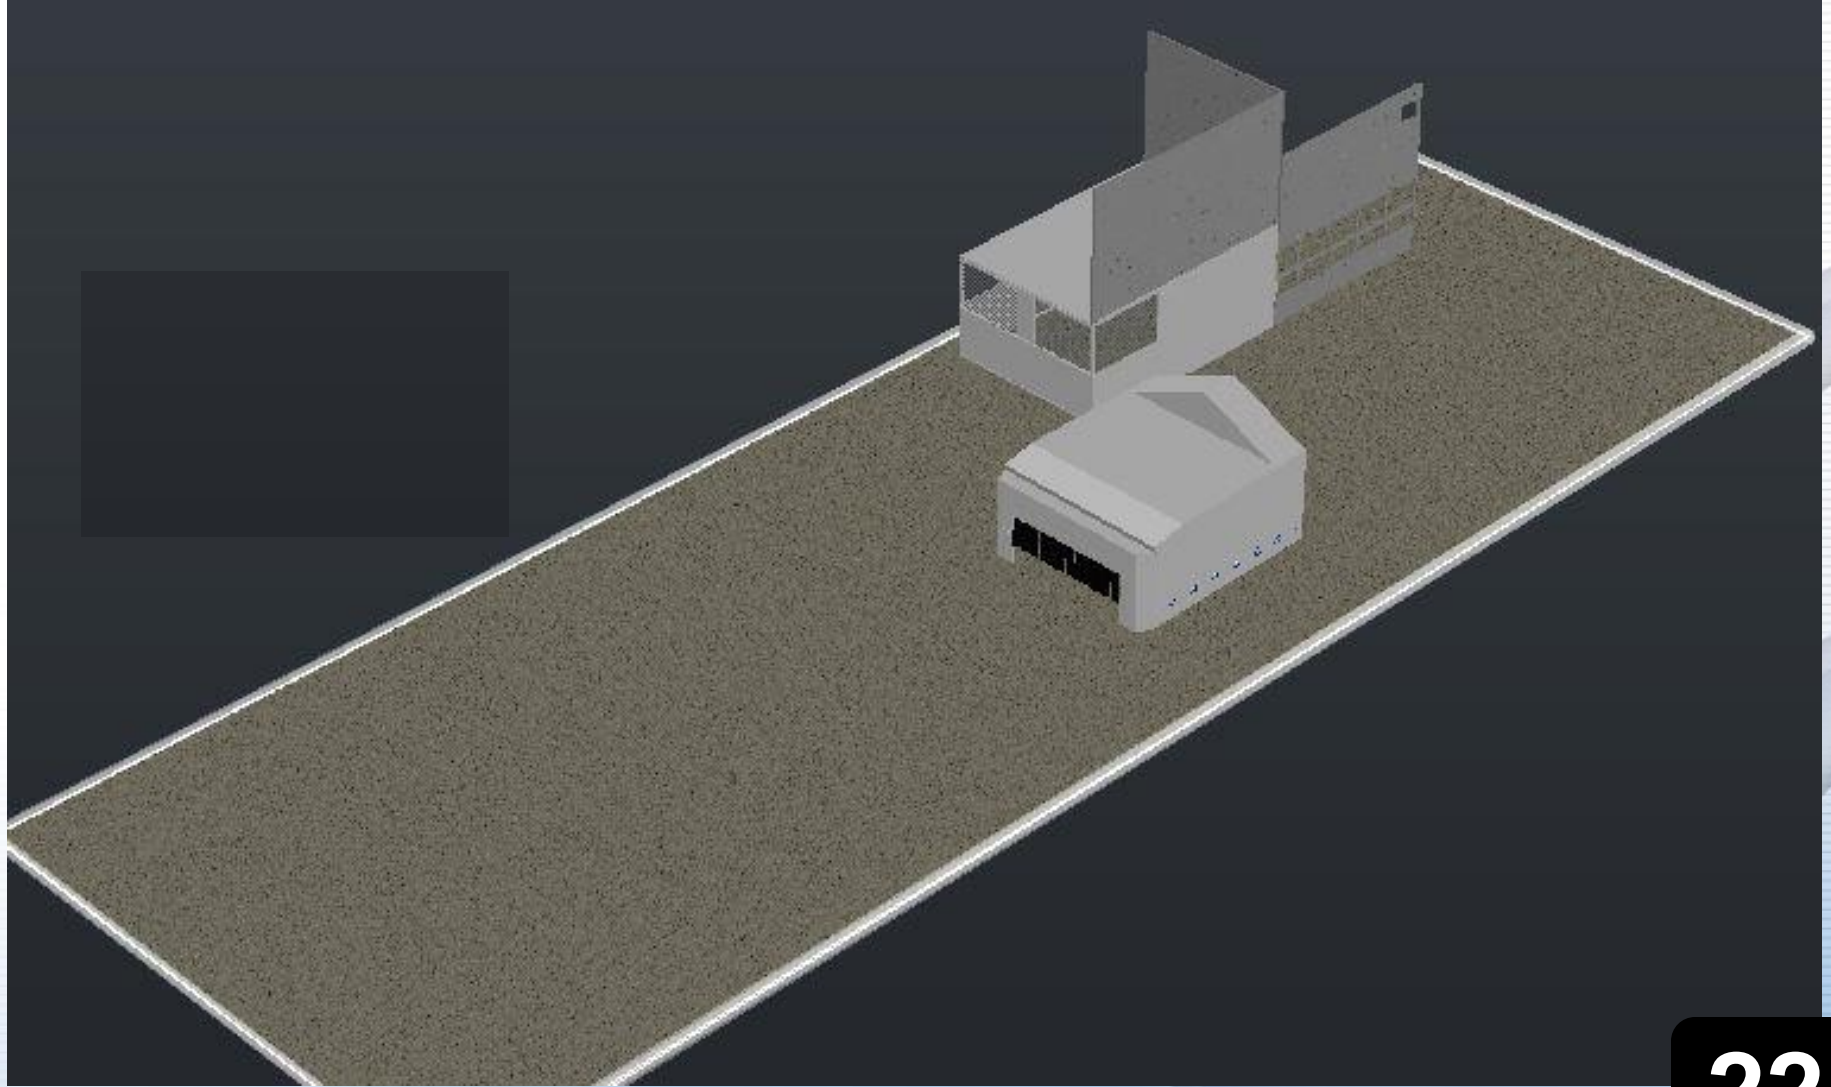


T-side of SB room



M-side of SB room



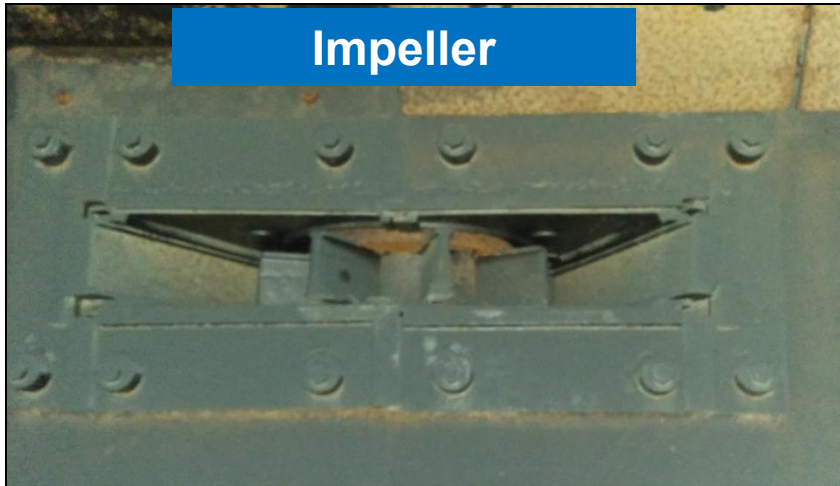

PHASE 5


❑ Removal of paint machine from top to bottom

NO. OF DAYS:


2 DAYS

NO. OF WORKERS: **5 MECHANICAL | 1 ELECTRICAL**

MACHINE OVERVIEW

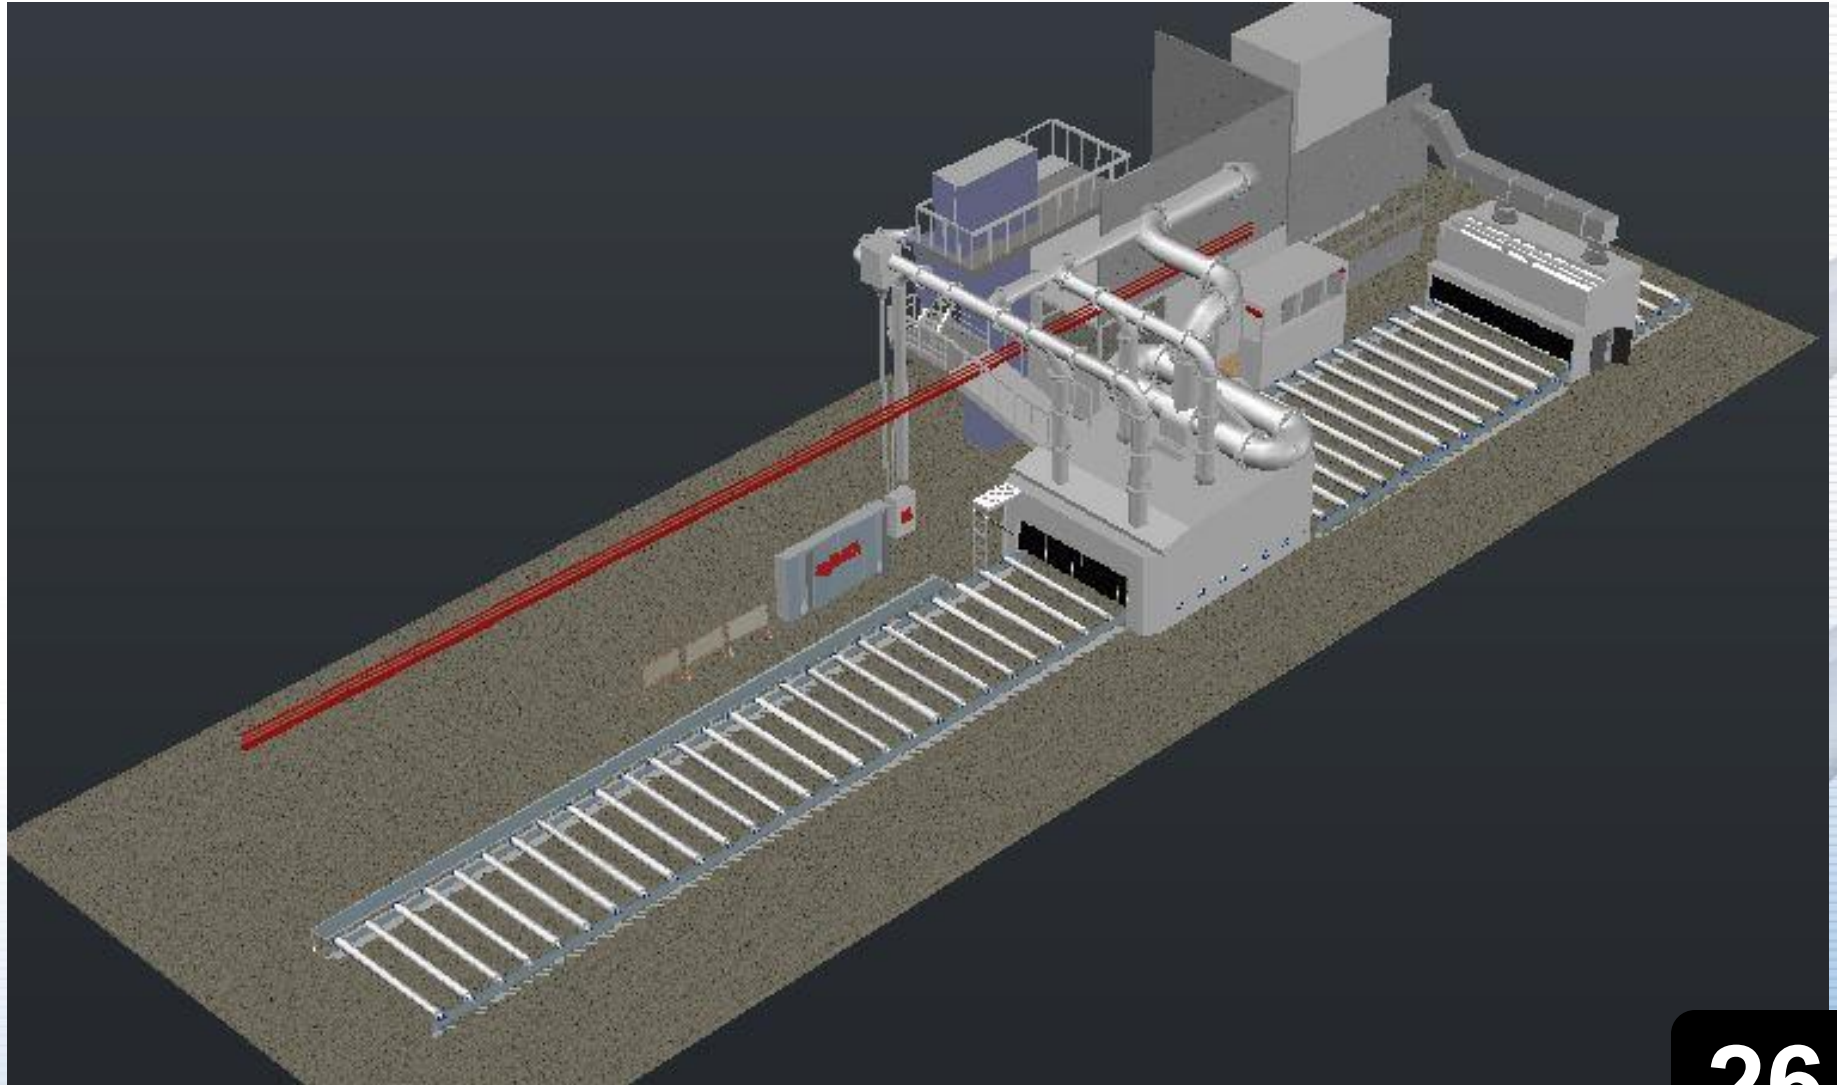

PHASE 5

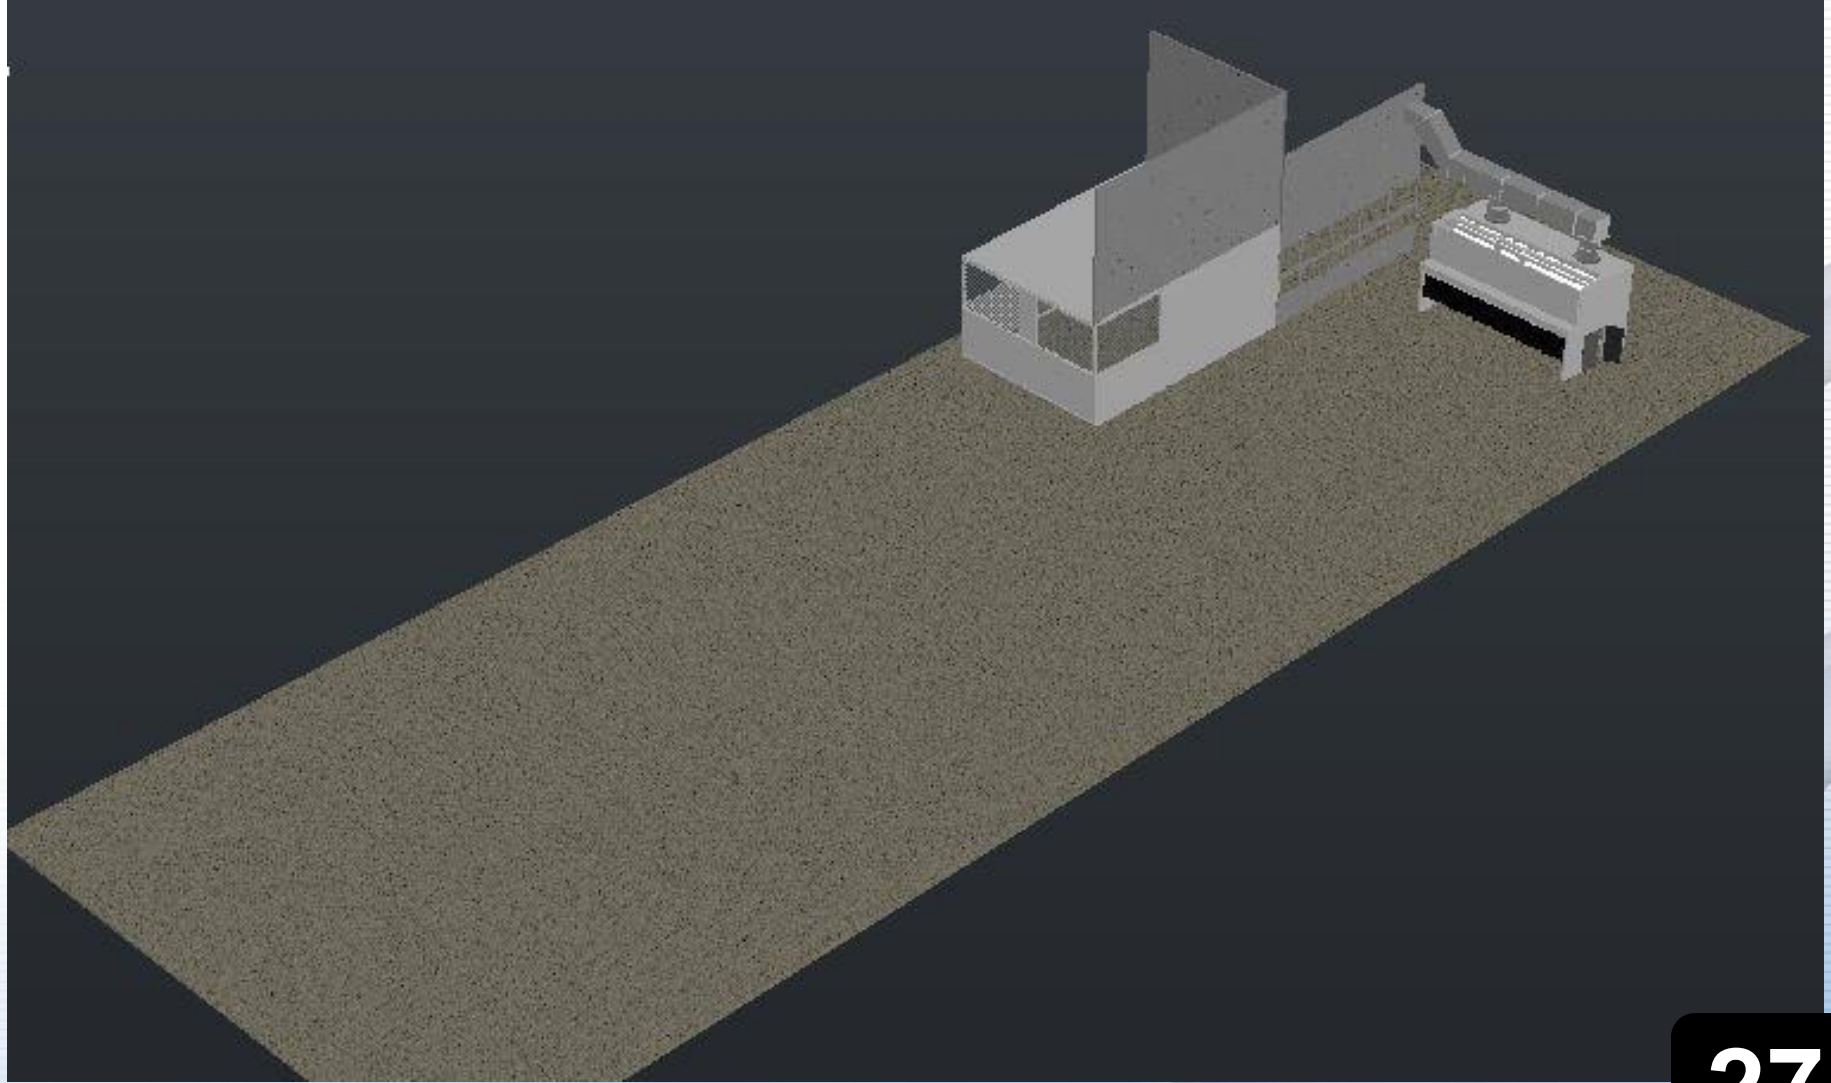


M-side of painting room




S-side of painting room



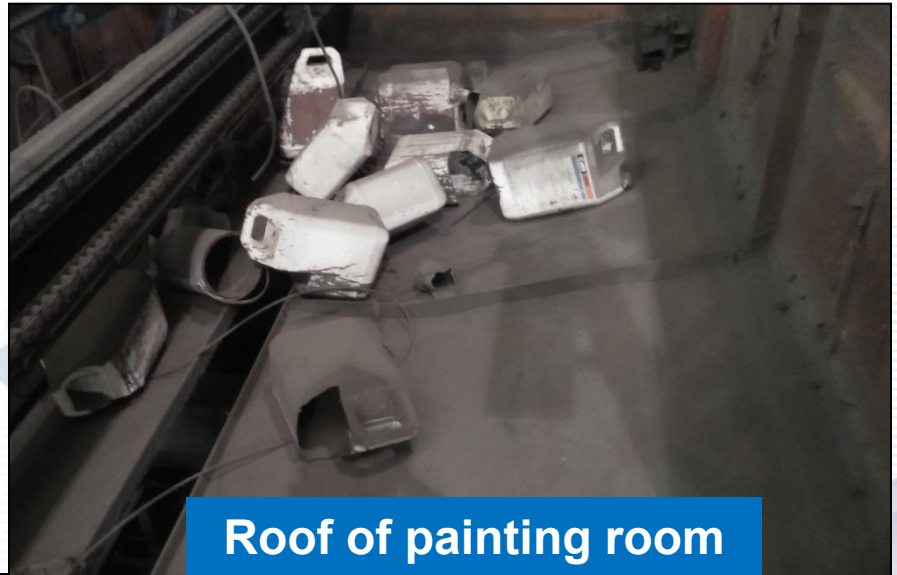

Roof of painting room

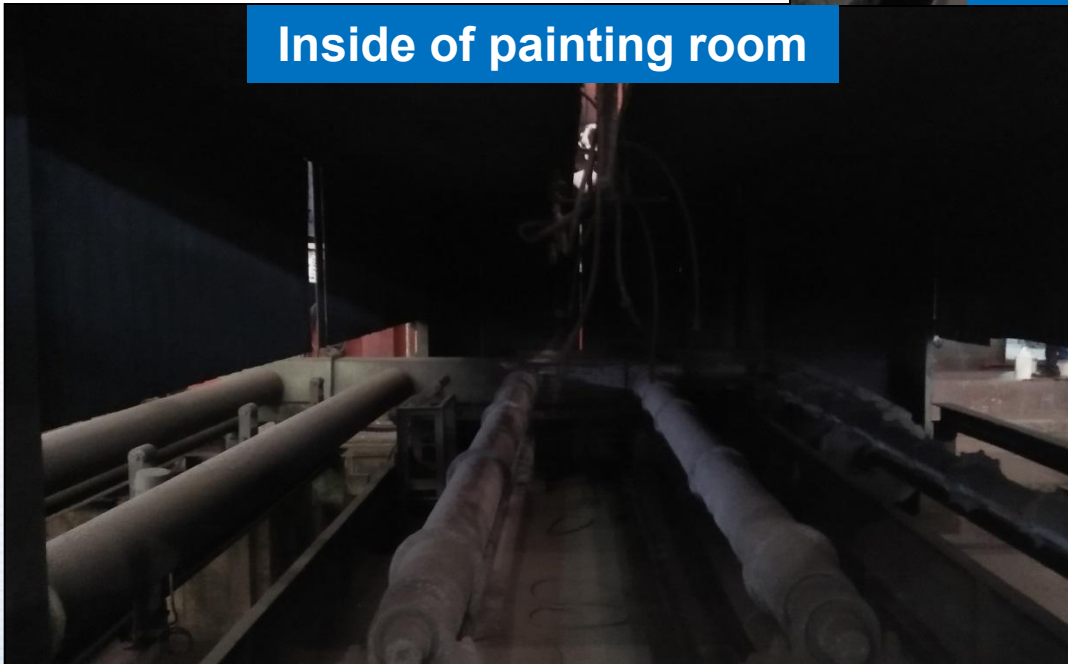

Inside of painting room

PHASE 6

- ❑ Removal of dust collector including remaining ducting beside Shotblast 2.


NO. OF DAYS:

6 DAYS


NO. OF WORKERS:

5 MECHANICAL | 1 ELECTRICAL

MACHINE OVERVIEW

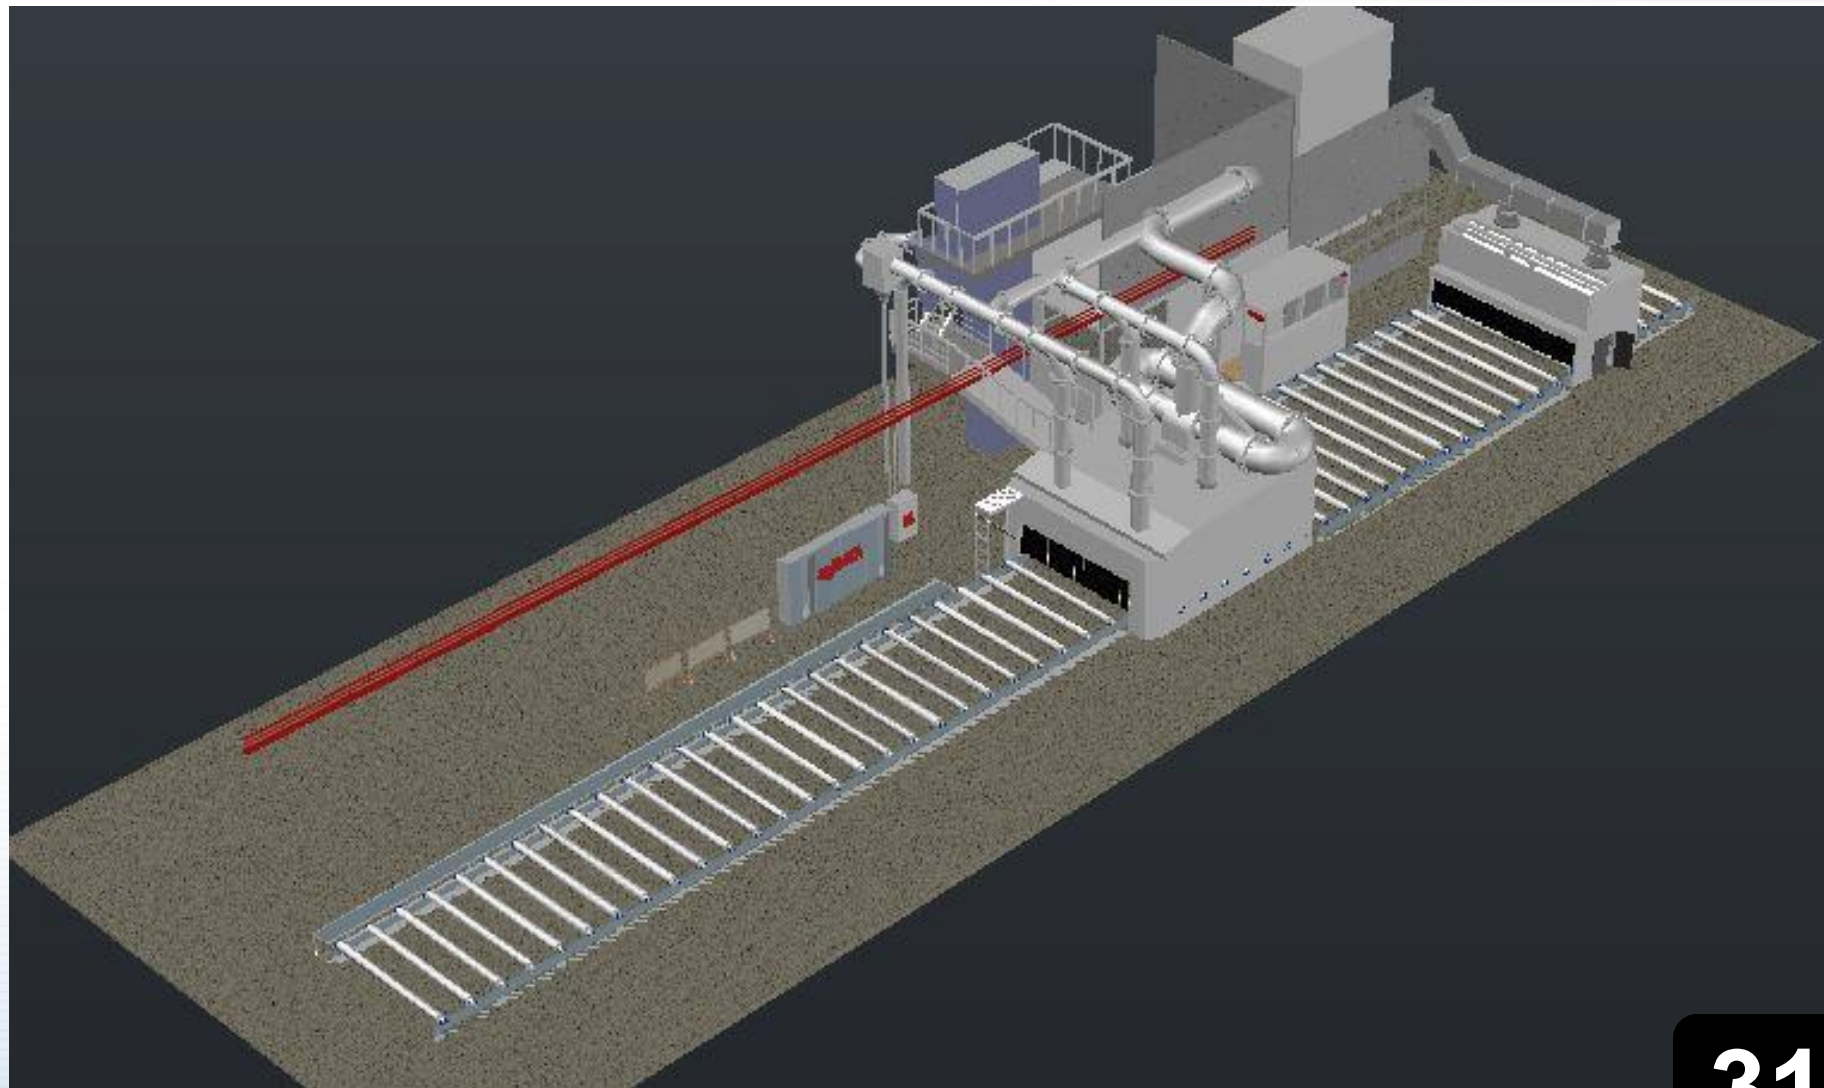

PHASE 6

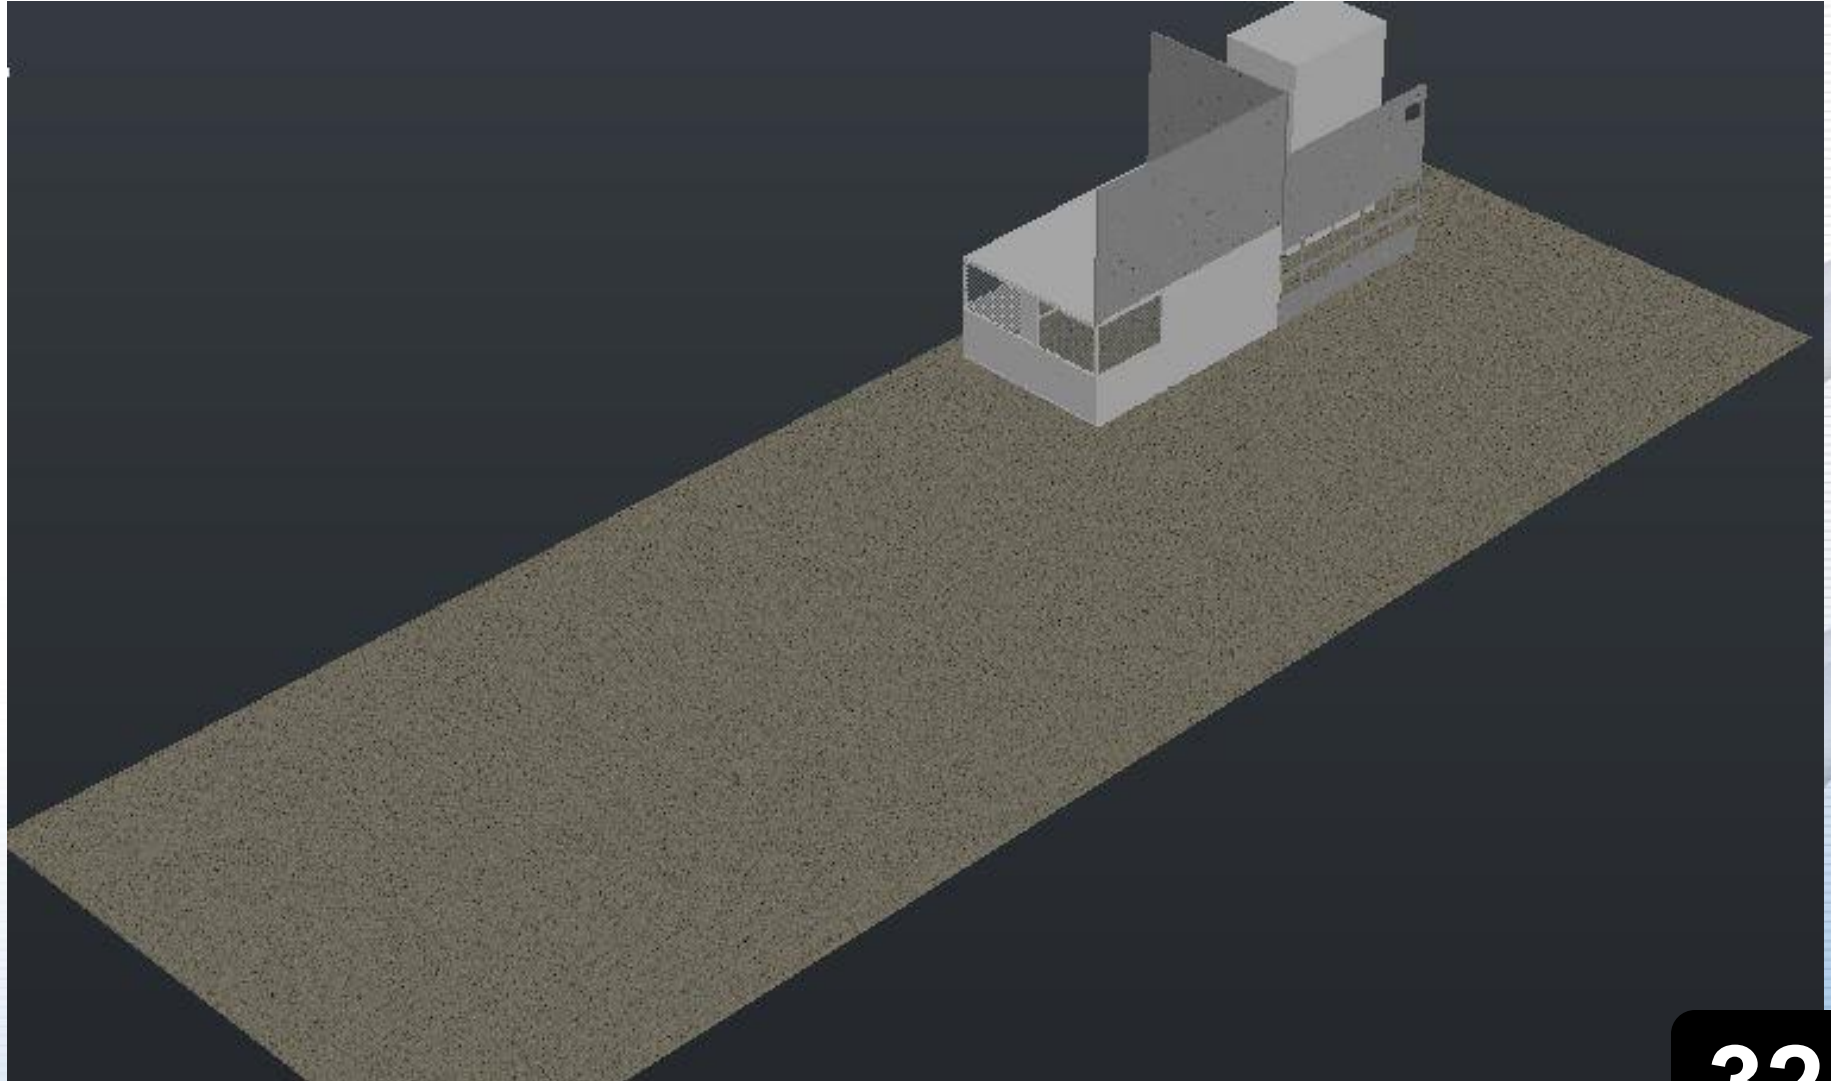

Remaining ducting



Remaining ducting





PHASE 7

❑ Cleaning and fencing

NO. OF DAYS:

1 DAY

NO. OF WORKERS:

4 MECHANICAL


Trash




Existing fence




DISMANTLING SEQUENCE

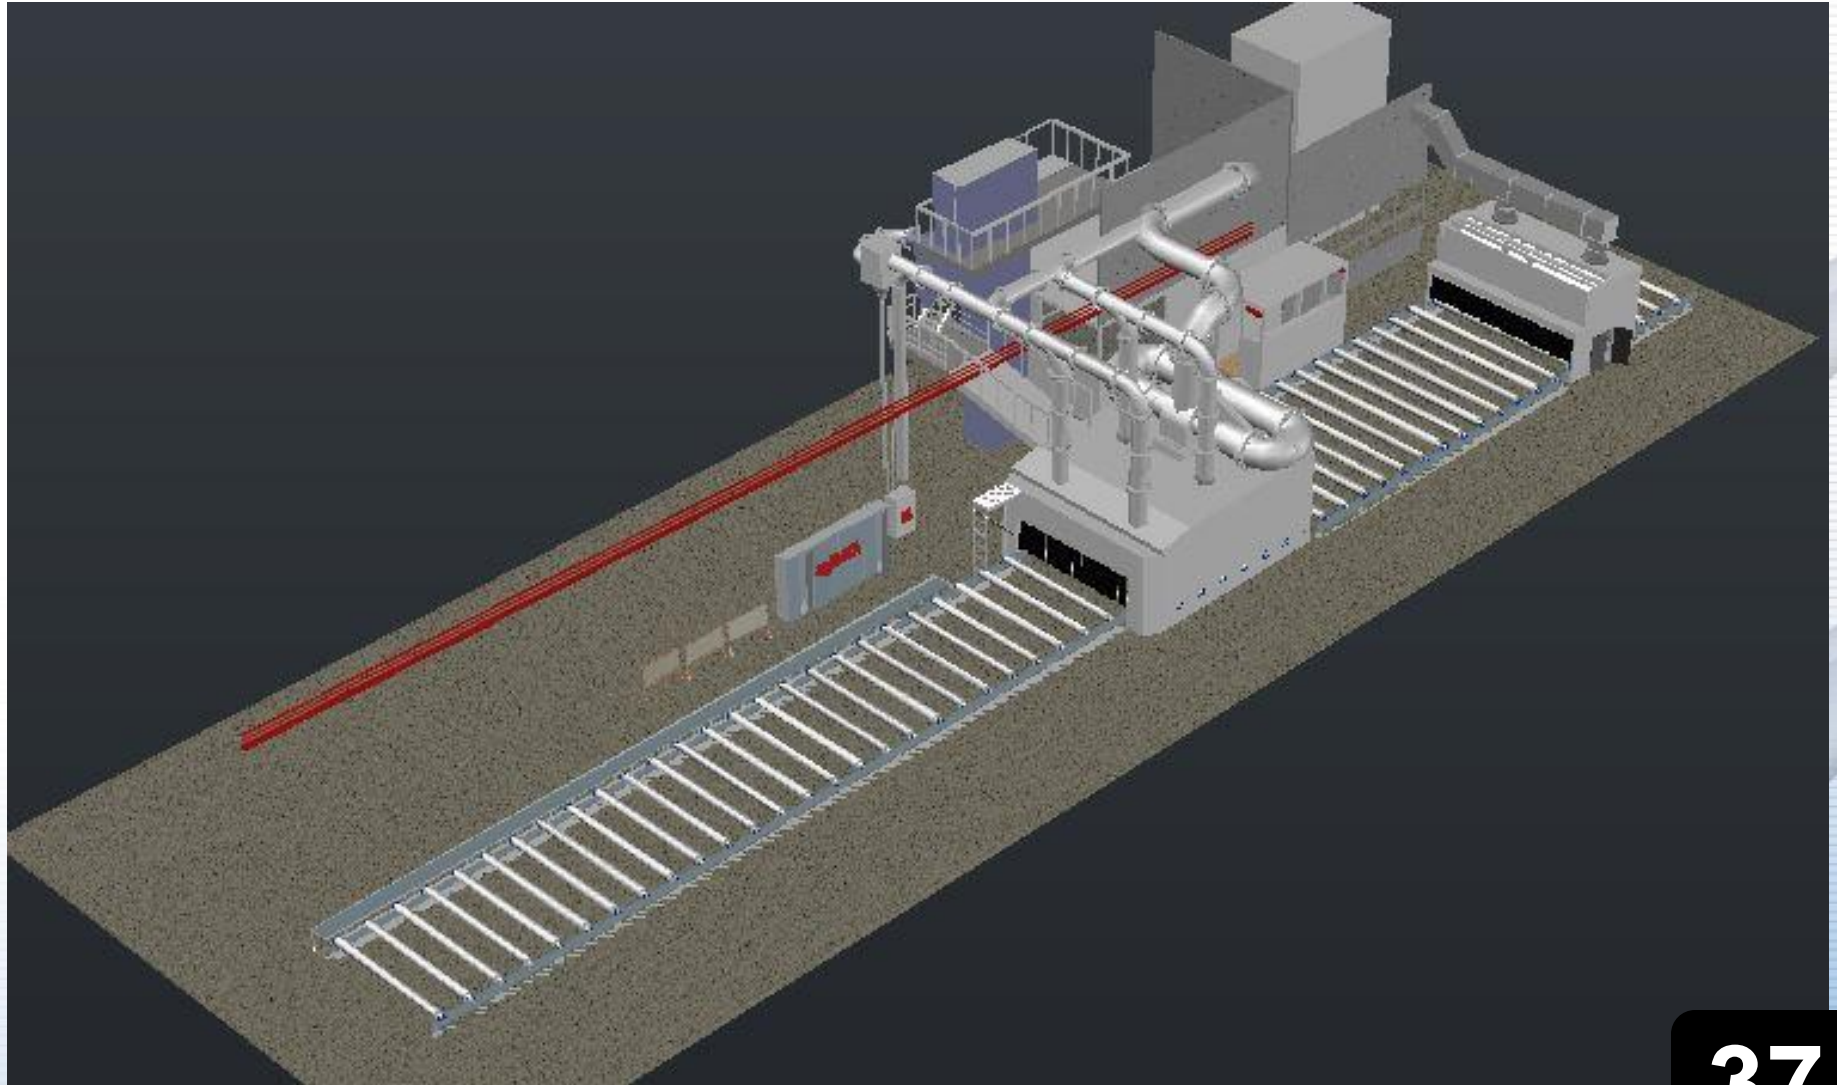


After PHASE 1

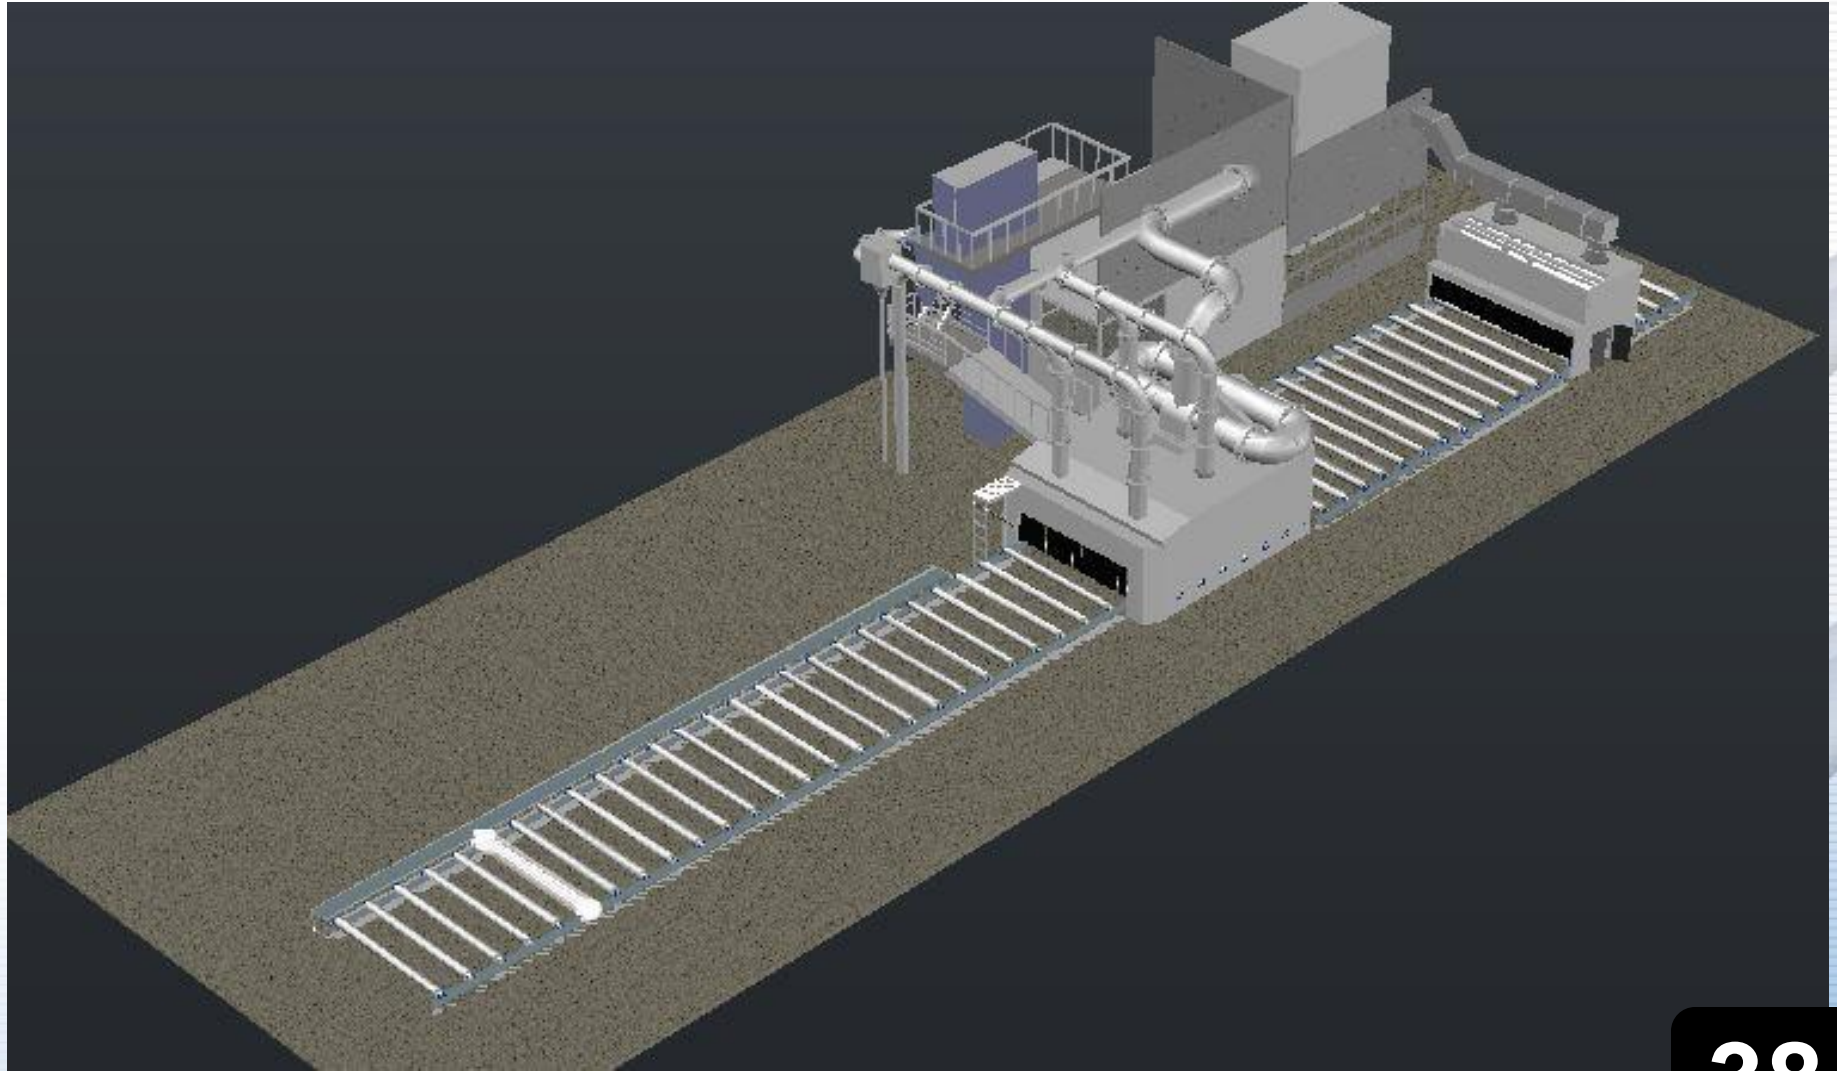


After PHASE 2

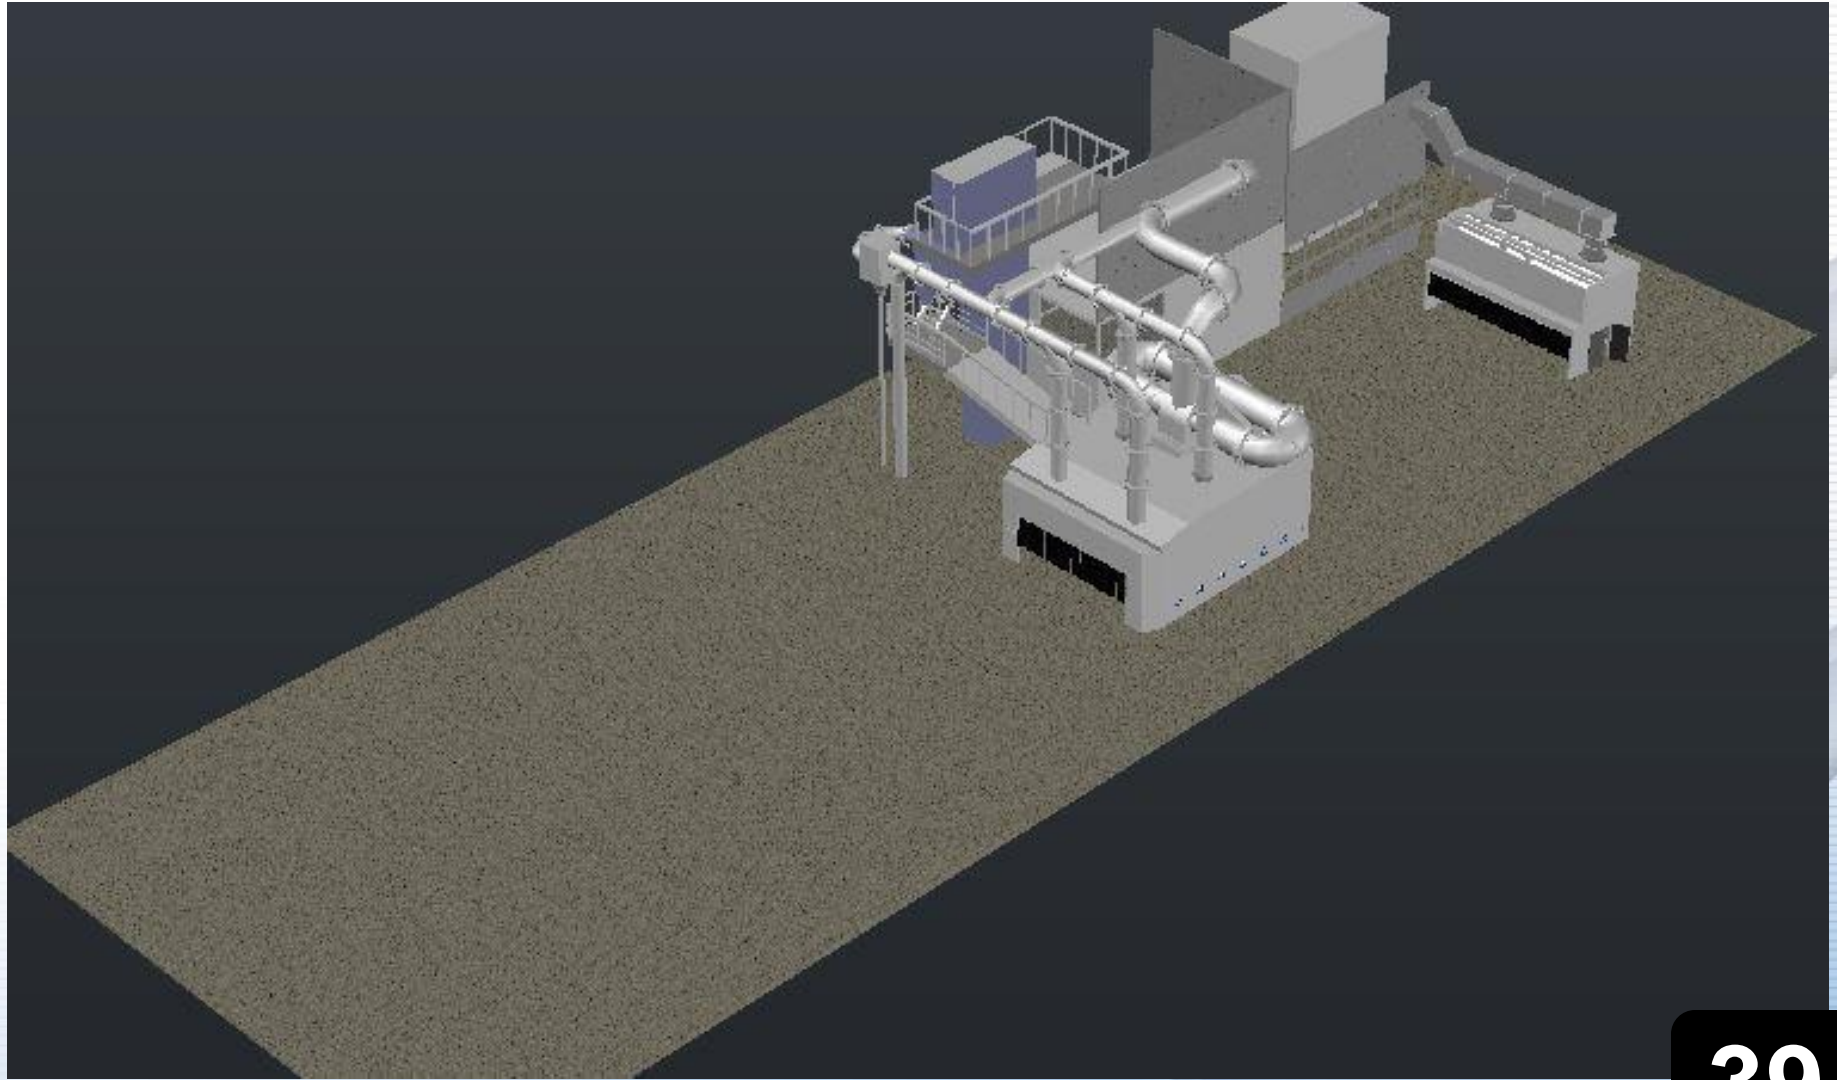


After PHASE 3

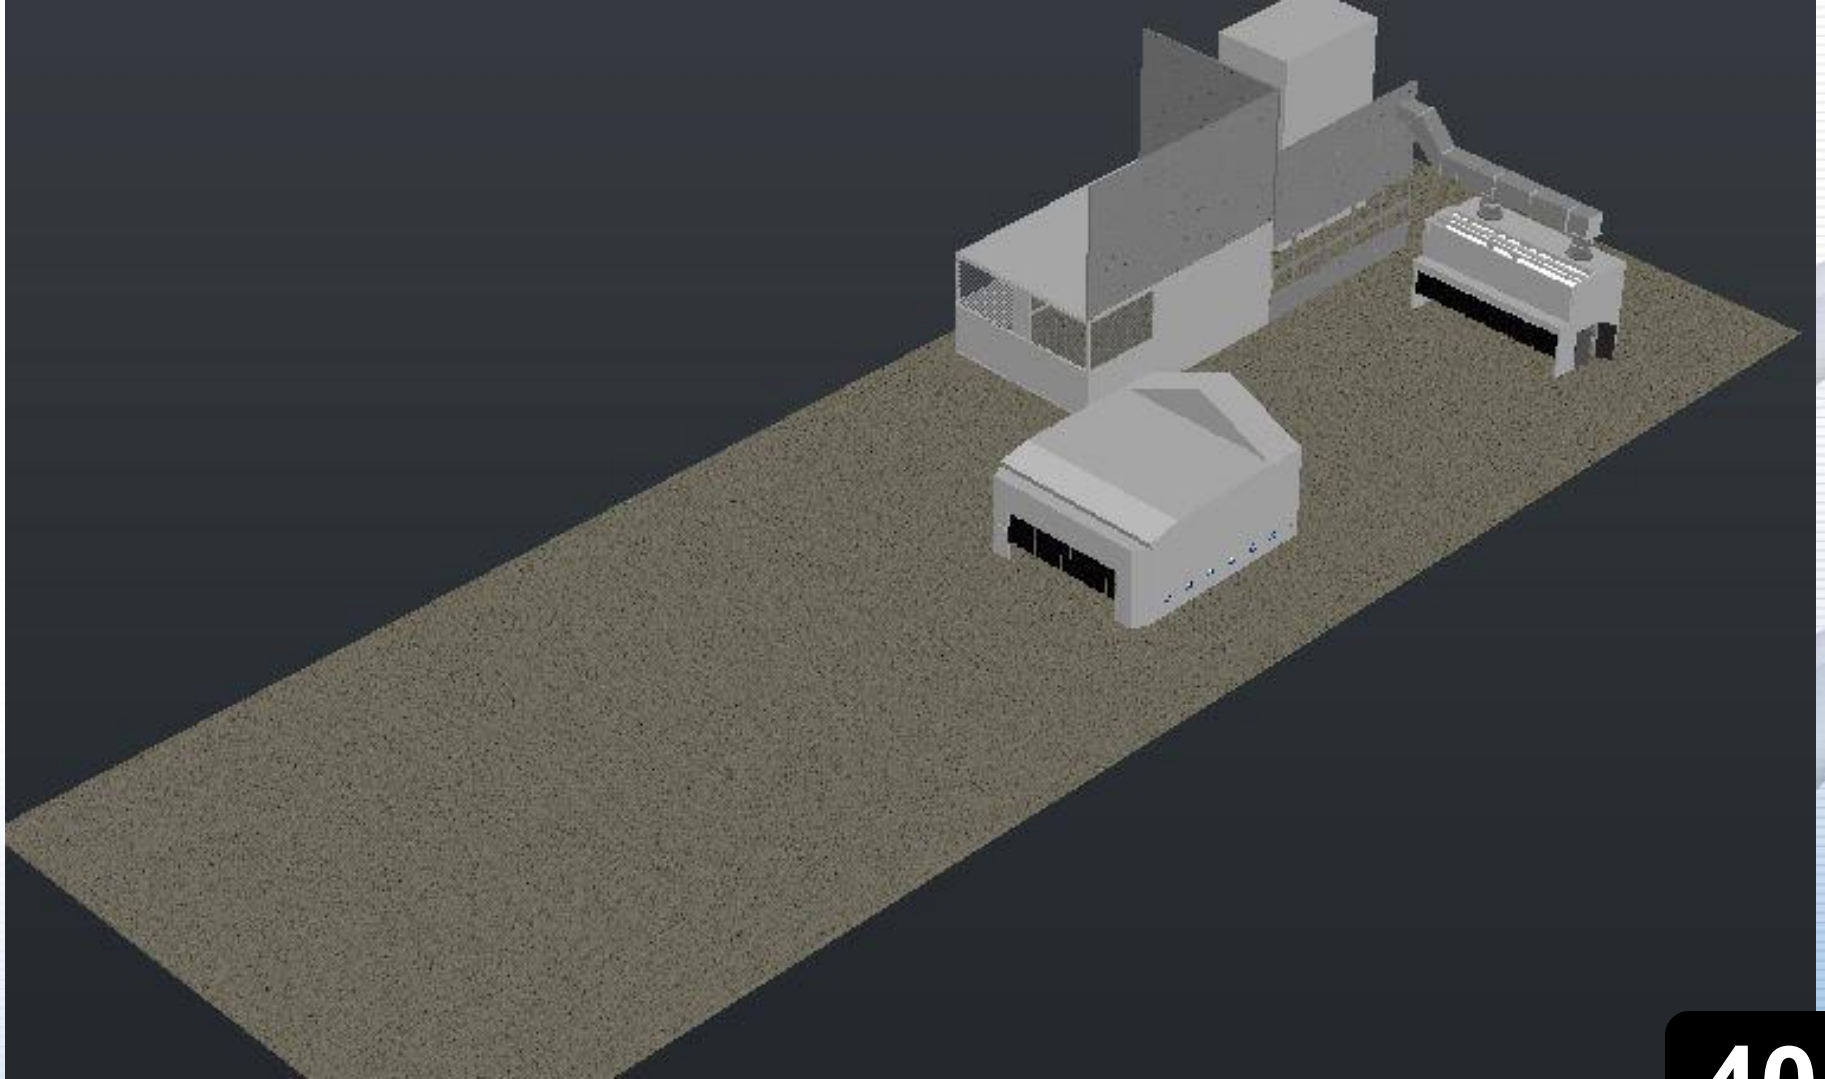


After PHASE 4

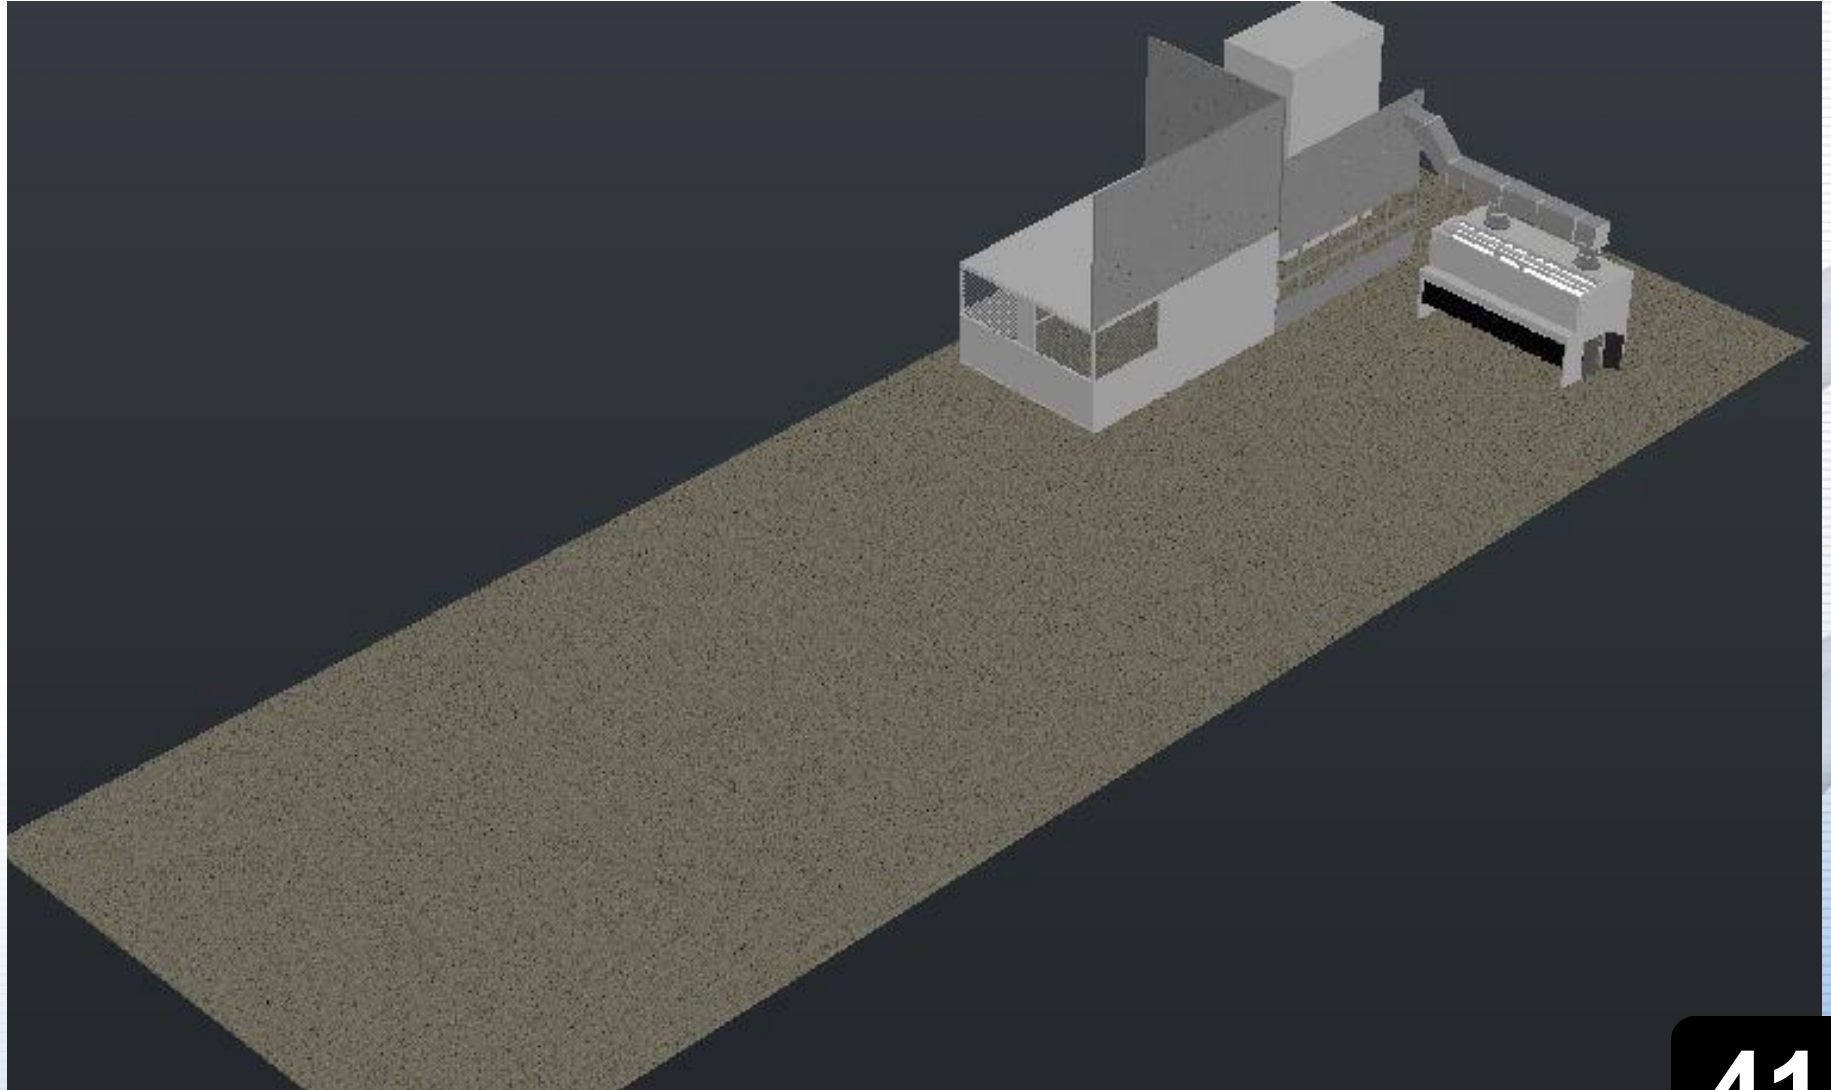

After PHASE 5

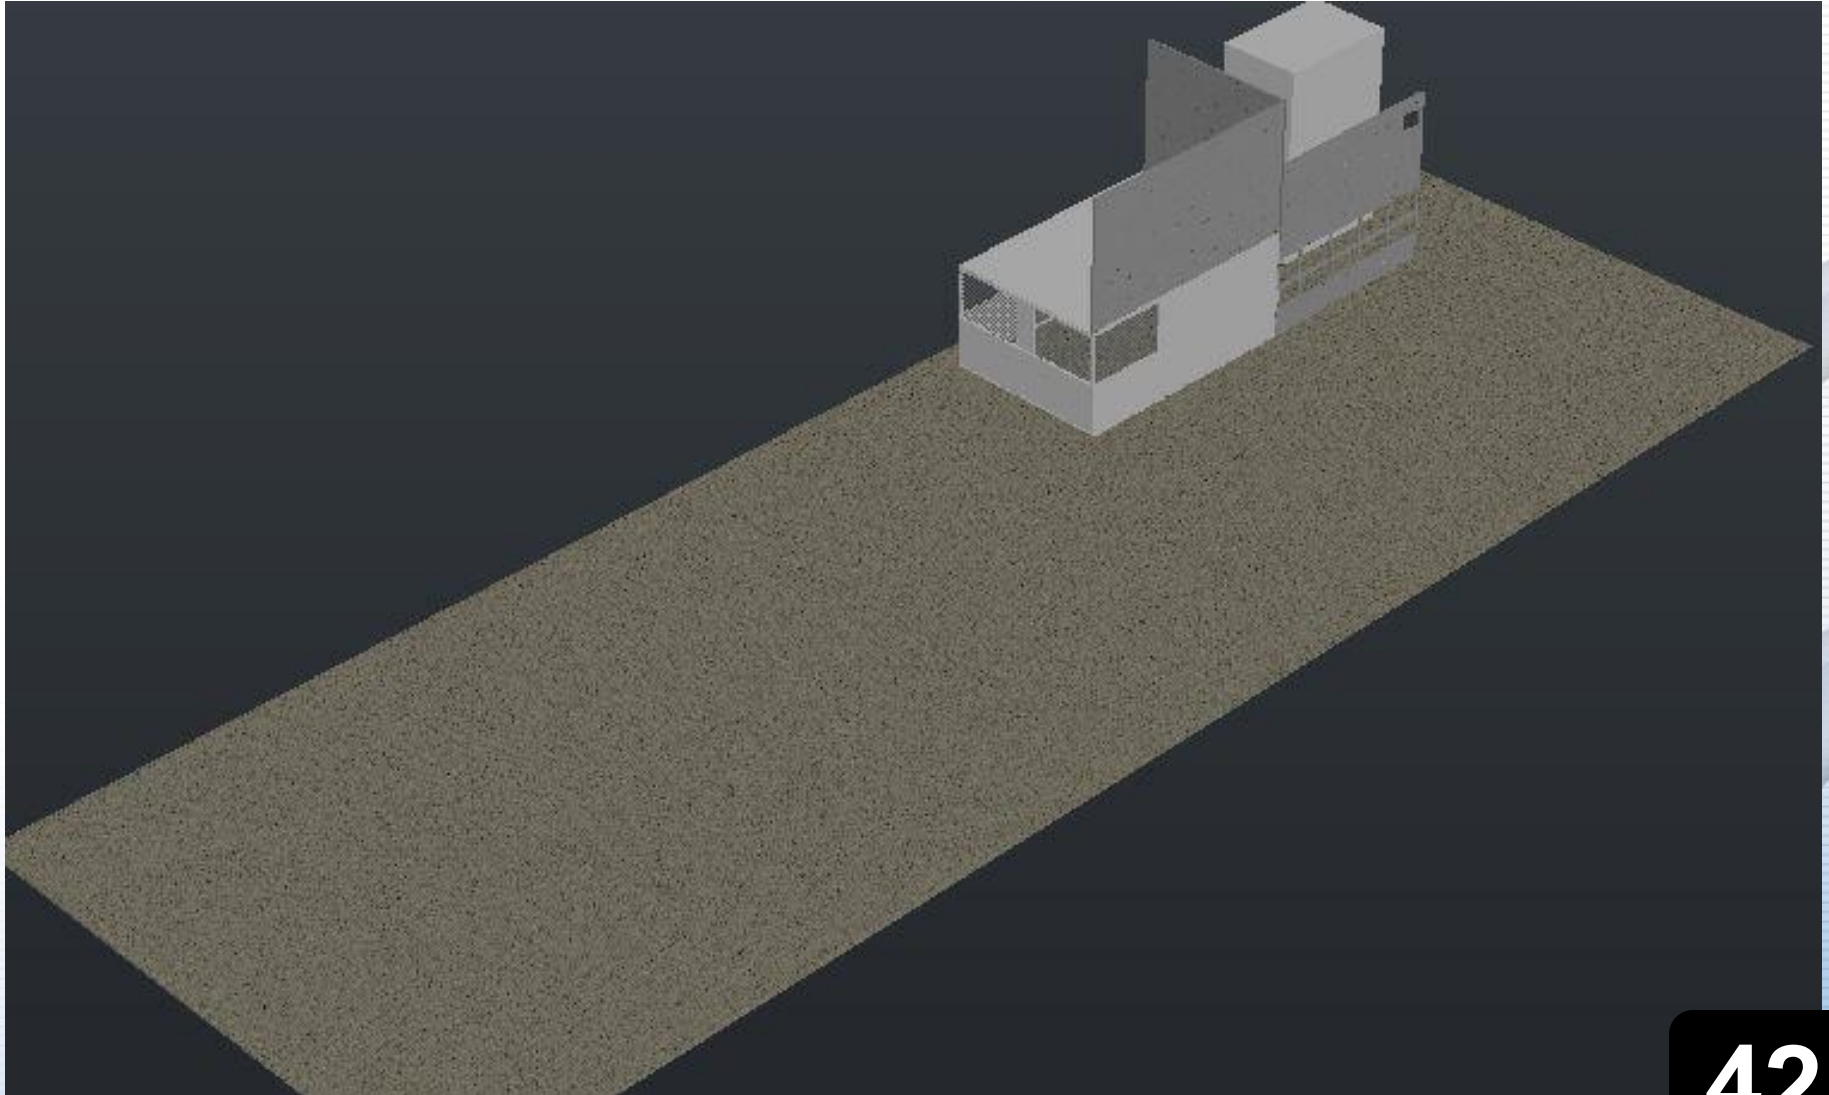

After PHASE 6

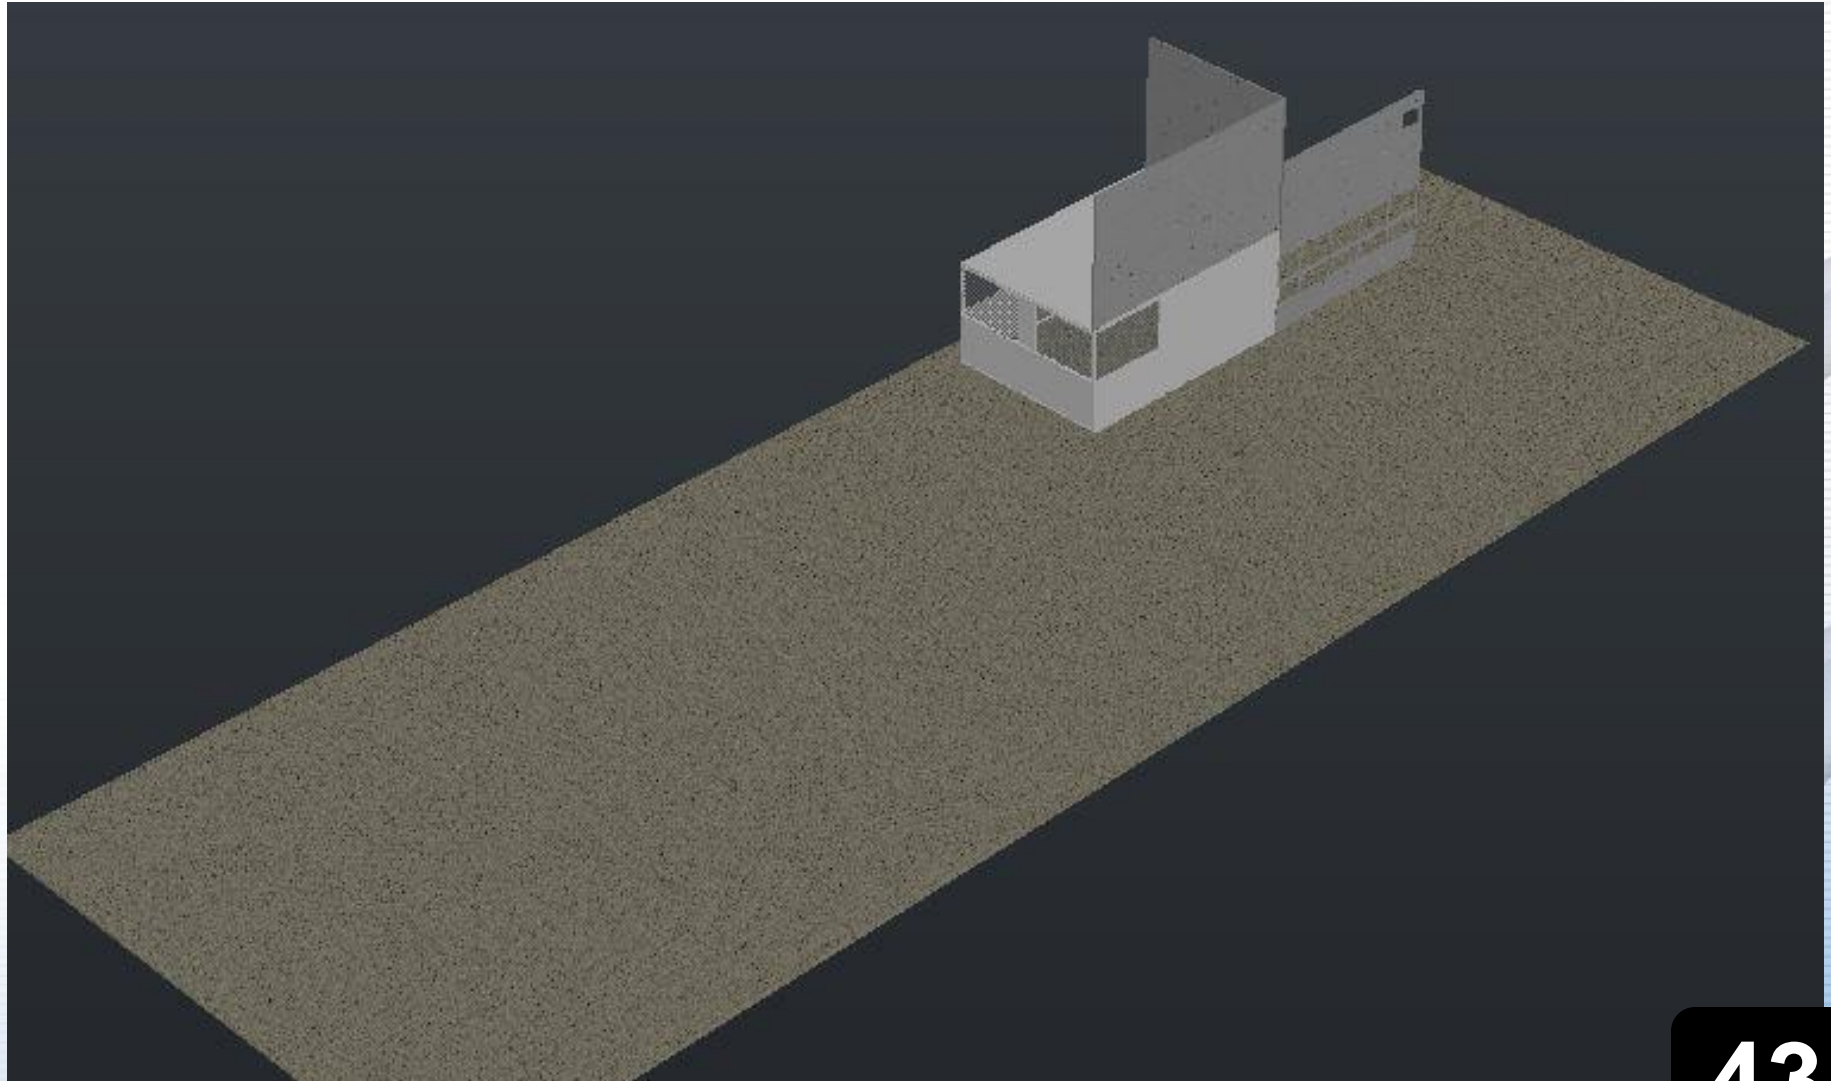

SAFETY EQUIPMENT

ITEM	QUANTITY
FULL PPE	-
Rubber gloves	4
Fire extinguisher	5
Blower	2
Fire hose	1

Others: **WORK PERMIT**

TOOLS & EQUIPMENT

ITEM	QUANTITY
Tester	2
Long handled wire cutter	2
Ladder	2
Trolley	1
Impact wrench	3
Demolition hammer	3
Cutting torch	4
Wrenches	-
Penetrating oil	13
Chain block	-

TOOLS & EQUIPMENT

ITEM	QUANTITY
Trailer truck	1
Mobile crane	1
Skymaster crane	1
5 hp, 5 m head pump	1
Scaffolding	-
Lighting	-
Cleaning blower	1
Cleaning equipment	-
Water sprayer	1
Overhead crane	1

Standard Working Procedure

1

Clean the area from dust and littered objects.

2

Prepare all the safety equipment and tools and equipment.

- ✓ Check fire extinguisher
- ✓ Connect the fire hose
- ✓ Set the cutting torches
- ✓ Set the blowers
- ✓ Install the lightings
- ✓ Install the scaffolding
- ✓ Place the scrapbox

Standard Working Procedure

3

Spray all bolted connections with penetrating oil, then wrench.

4

Identify the parts to be preserved and mark all sections to be cut.

5

Cut all the markings starting from top to bottom.

Standard Working Procedure

6

Cut all scrap to size containable in the scrapbox

7

Place all the removed parts to the stock area.

8

Note all removed parts in the checklist.

Temporary stock area inside



Stock area outside



SCHEDULE

Item No.	Work Description	plan / actual	JULY							AUGUST																							STATUS								
			23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21		22	23	24	25	26	27	28	29
1	Final Discussion to Sub-contractor (JEC)	plan	→																																						
		actual																																							
2	Sub-contractor (JEC) preparation	plan	→																																						
		actual																																							
3	R & R preparation, submission and approval	plan			→																																				
		actual																																							
4	Tools and Equipment preparation and request	plan			→																																				
		actual																																							
5	PHASE 1	plan								→																															
		actual																																							
6	PHASE 2	plan										→																													
		actual																																							
7	PHASE 3	plan																			→																				
		actual																																							
8	PHASE 4	plan																											→												
		actual																																							
9	PHASE 5	plan																												→											
		actual																																							
10	PHASE 6	plan																														→									
		actual																																							
11	PHASE 7	plan																																							→
		actual																																							

ARIGATU
GUSAIMAZO
